
# Kitchen | Mark the bases

**WORKING MARKOUT · VERIFY IN FIELD · NOT A CUT RELEASE**

K-M01 R1 crop · NOT TO SCALE · shared SOUTH/EAST finished corner = 0



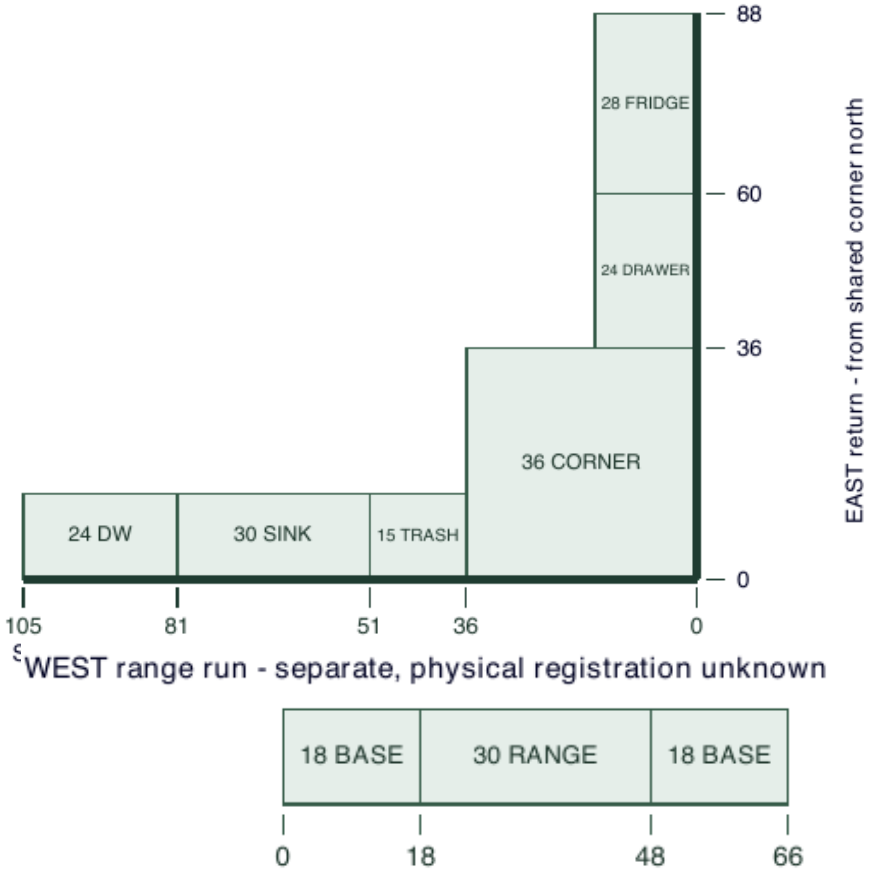


P02 · Oct 26: right opening is a CANDIDATE; Monday's door is not identified. Keep left opening and window.

**Verify faces, jambs, services and endpoints before framing.**

---

**1 Find the faces**
Confirm the shared finished corner and the separate west start; do not scale the drawing.

**2 Tape the stations**
Crew marks K-M01 on the floor. John OR Tisa checks every station, dates a photo and records conflicts.

**3 Identify the door**
John identifies the intended opening on site; P02 is only a candidate. Measure jambs and services.

**TOOLS / NEXT**
Check tape measure, removable tape or chalk, marker and phone. After reviewed framing, electrician checks box positions and routes.

**STOP / REVIEW: Do not cut or frame an unidentified opening or unresolved service, wall face or clearance. Lead records the reviewed sheet, decision and date.**
