
UNIT 4 | D04 DINING WEST WALL

PANEL + PICTURE-FRAME COORDINATION | 01 NOV 2026 | R1

REVIEW ONLY — NO FRAMING OR CUT RELEASE

WALL ELEVATION • NOT TO SCALE

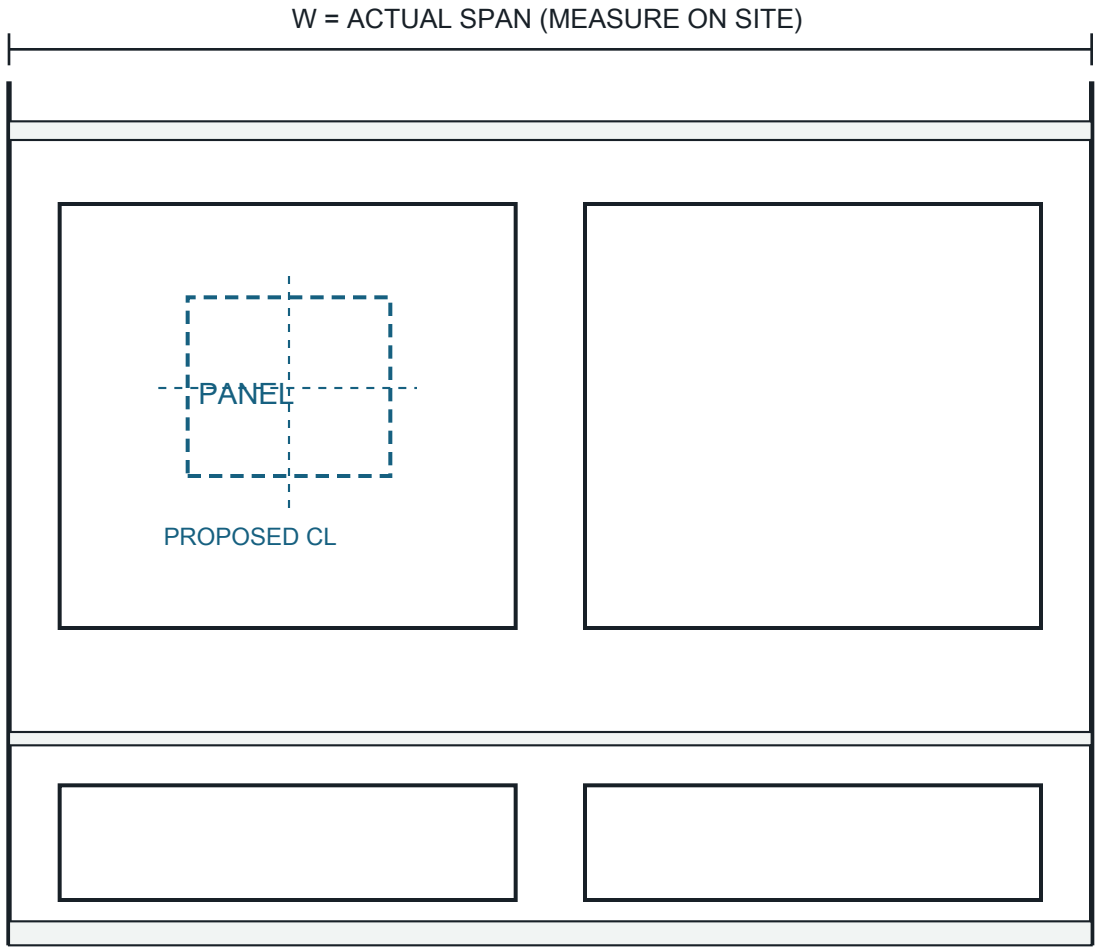

LEFT: OUTER EDGE, RIGHTMOST CASING

RIGHT: INSIDE CORNER

W excludes the transom door on the perpendicular wall.

Upper frames: 41–99 in AFF; lower: 13.5–31 in AFF.

Vertical dimensions are proposed, not field measurements.

Dashed panel is schematic only; not a cover or framing outline.

PANEL PAUSED: no charge Nov 1; no automatic Nov 2; approve quote/payment.

PANEL POSITION

x = W/4 + 1 in from left datum

Target CL = 65 in AFF; can/cover TBD

Both are proposals; not field marks.

Finished-floor / subfloor offset: UNKNOWN.

FRAME STRING

4 + B + 4 + B + 4 = W

B = (W – 12) / 2; numeric W unknown.

Two upper + two lower frames.

High rail and chair rail shown schematically.

EQUIPMENT

Eaton BRP20L125G • 20 spaces

Published candidate cover BRPX2A20L1F:

22 in high × 15.3 in wide.

Verify included trim and actual fit in hand.

BEFORE FRAMING

1. Actual box AND matching trim in hand.
2. Verify W, wall depth, studs, floor datum.
3. Electrician confirms cover removal, door swing, working space and feeder.
4. Rough opening: NOT DETERMINED.
5. Coordinate D5 and D02 cabinet return.

D04: window casing to right inside corner; transom door is on adjacent wall.

Source: Living/Dining Review R2 pp. 3–4, 11, 13; Eaton product and cover references. No site measurements certified.


UNIT4 D04 dining entry wall and subpanel

Schematic elevation and horizontal section for framing, flush trim and finish coordination

1 DINING ENTRY WALL ELEVATION

NONSCALE

[A] Approximate X2 body for PLANNING ONLY - not rough opening / cuts; verify actual can.

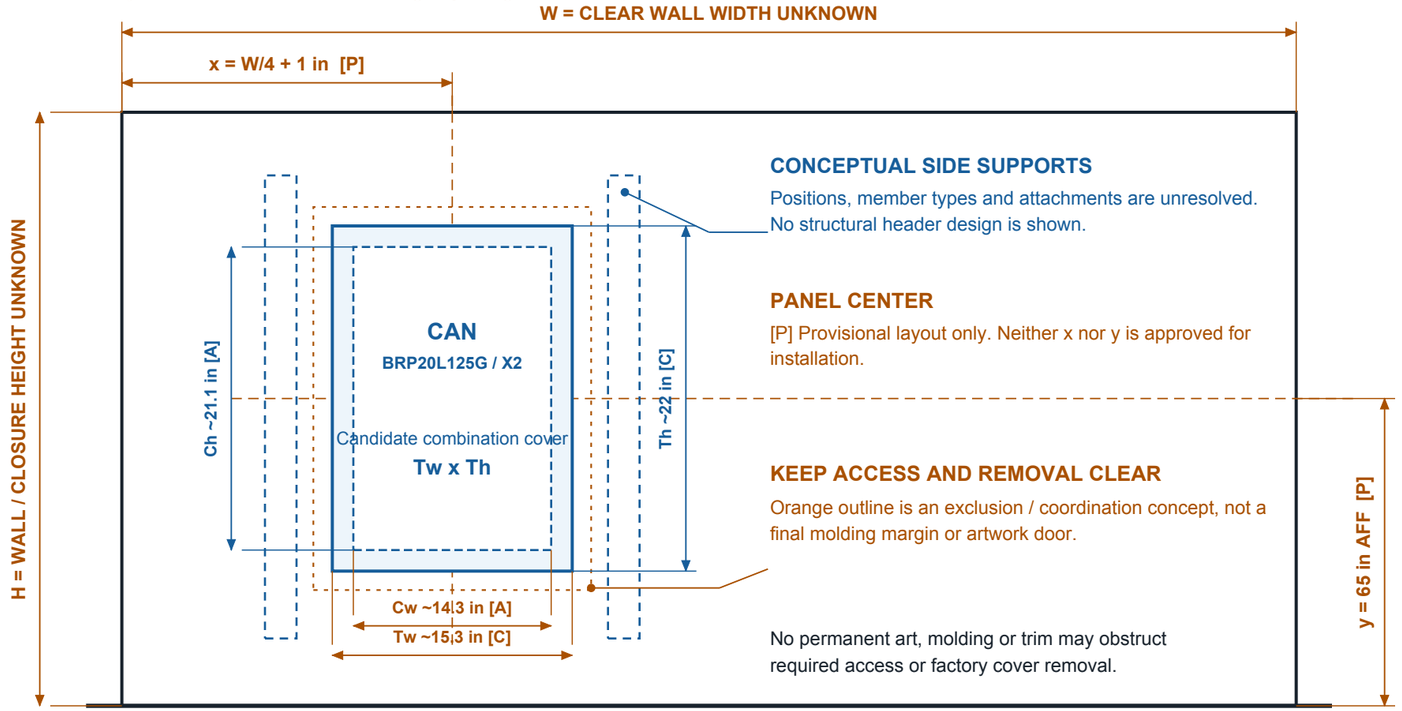

CONCEPTUAL SIDE SUPPORTS

Positions, member types and attachments are unresolved. No structural header design is shown.

PANEL CENTER

[P] Provisional layout only. Neither x nor y is approved for installation.

KEEP ACCESS AND REMOVAL CLEAR

Orange outline is an exclusion / coordination concept, not a final molding margin or artwork door.

No permanent art, molding or trim may obstruct required access or factory cover removal.

FINISHED FLOOR DATUM

Existing wall / opening limits require field verification.

LEFT DATUM A: WINDOW CASING


R2 datum: outside edge of rightmost window casing. W ends at right inside corner. Field-measure before layout.

2 HORIZONTAL SECTION AT PANEL

NONSCALE - room side is below

[A] PLANNING BODY ONLY - NOT RO / CUTS

SYMBOLIC REAR / CAVITY SIDE

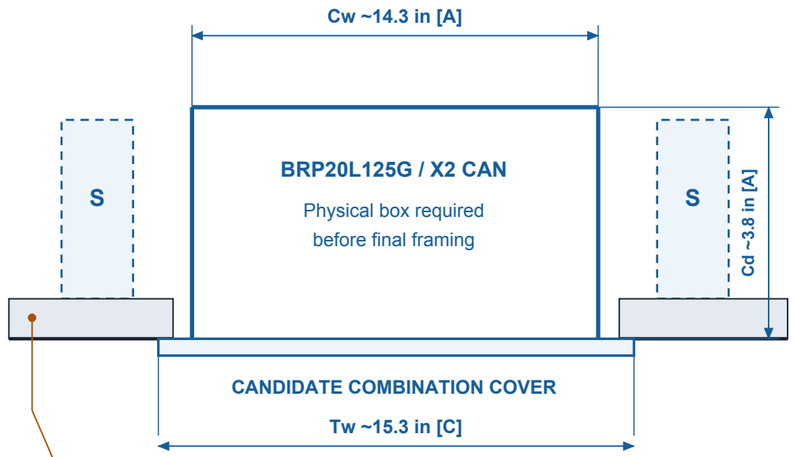

t = TOTAL FINISH BUILDUP UNKNOWN

Mounting depth is to be coordinated with actual can, listed matching factory trim / cover and the final finish plane by the electrician.

S = CONCEPTUAL SUPPORT ONLY

No support width, spacing, stud count, structural size or fastening schedule is conveyed by these symbols.

BEFORE ANY FRAMING RELEASE

Have the selected physical box and matching factory trim / cover in hand. Confirm wall measurements, panel position, finish buildup and mounting details; then obtain the existing design lead's reviewed framing layout.

DRAWING KEY

- Black - existing bounds, schematic
- Blue - proposed / unreleased coordination
- Orange - unresolved / provisional

[P] = provisional, not approved

[A] = approximate body; [C] = published candidate cover

NOT FOR PERMIT, CONSTRUCTION OR PROCUREMENT

No structural header sizing, stud cuts, cutlist, equipment approval or code approval is provided.

Geometry is symbolic. Do not scale or derive dimensions from drawn proportions.

REVIEW ISSUE

2026-11-01 | Review R1

Scale: NONSCALE

UNIT4 / D04

FC-01

UNIT4 D04 dining entry wall and subpanel

Dimensions, source limitations and release checklist for the existing Unit4 design lead

3 DIMENSION AND EQUIPMENT REGISTER

VARIABLE / ITEM	STATUS AND REQUIRED RESOLUTION
W / H	Unknown. W: outside edge of rightmost window casing to right inside corner, facing D04. Door is on the perpendicular wall.
x = W/4 + 1 in	PROVISIONAL. From the outside edge of the rightmost window casing, facing D04. Field-check W.
y = 65 in AFF	PROVISIONAL. 65 AFF target; identify whether can or cover center. Confirm finished-floor datum.
Cw / Ch / Cd	Planning body per X2: approx. 21.1 H x 14.3 W x 3.8 D in. Verify actual can. Catalog SKU values differ slightly. Not RO / cuts.
Tw / Th	Candidate BRPX2A20L1F cover published as 15.3 W x 22 H in. Verify actual included cover, fit and removal in hand.
t / mounting depth	Unknown finish buildup. Coordinate layers, final plane and box mounting depth with electrician.
Panel selection	Current user preference: Eaton 20 full spaces. Working candidate BRP20L125G, 125A main-lug-only; qualified breaker / termination review pending.
Molding / artwork	R2 proposes 2 upper / 2 lower frames: 4 + B + 4 + B + 4 = W; B=(W-12)/2. Access and molding fit unverified.

CANDIDATE BODY DIMENSIONS ONLY - NOT CUT DIMENSIONS

X2 drawing: ~21.10 H x 14.30 W x 3.80 D in. SKU raw axes: L/D 21; H 3.88; W 14.31 in.

Use X2 for planning orientation only; resolve numeric discrepancy on actual can. Candidate cover 15.3 x 22 in; actual cover / final RO unverified.

4 REVIEW HOLD POINTS

- ☐ **Field geometry and datum**
  Measure D04 W from rightmost window casing outer edge to right inside corner; verify H and finished-floor datum.
- ☐ **Existing opening and structural status**
  Responsible professional reviews the existing opening and structural condition before alterations. Resolve header / support design separately.
- ☐ **Box and trim physically available**
  Select exact model and matching factory trim / cover; verify actual can / cover dimensions and mounting provisions before final framing.
- ☐ **Electrical design verification**
  Electrician verifies ratings, mounting depth, required working access, grounding / neutral arrangement and installation details.
- ☐ **Access and finish coordination**
  Maintain required access, cover removal and operation. No permanent artwork or molding obstruction; coordinate finish buildup.
- ☐ **Design lead release**
  Existing Unit4 design lead reconciles direct sources, confirms D04 orientation / location and issues reviewed dimensions before release.

SOURCE AND CONFLICT REGISTER

S1 Oct 30 user instruction: the dining entry wall closure houses the electrical subpanel. S2 R2 pp. 3-4 and 11 define D04 dining west, frame formula, and casing-to-corner datum; field measurement pending.

S3 Older Rev A E11: approximately 12 in north of kitchen SE, living face. STALE CONFLICT - do not transfer to D04. S4 L01 living picture box 124 in is unrelated and is not D04 wall width. Original source URLs and current R2 reviewed; field measurement remains open.

S5 Eaton BRP20L125G SKU page

S6 Eaton BR catalog V1-T1-51 / V1-T1-75 (X2)

S7 Eaton loadcenter installation tips

Linked sources / full URLs in README

NOT FOR PERMIT, CONSTRUCTION OR PROCUREMENT

No structural header sizing, stud cuts, cutlist, equipment approval or code approval is provided.

Geometry is symbolic. Do not scale or derive dimensions from drawn proportions.

REVIEW ISSUE

2026-11-01 | Review R1

Scale: NONSCALE

UNIT4 / D04

FC-02
