Unit 4 Walls, Trim & Outlets

Room-by-room wall treatment, trim moulding and outlet plan. One section per room with site photos, wall mock-ups and a usability check of every outlet.

WORKING PLAN — not a cut, purchase or electrical release. Written dimensions govern; do not scale drawings. All heights in inches above finished floor (AFF).

Already settled — nothing to do

- One frame system for living and dining: chair rail 35–37, lower frames 13½–31, upper frames 41–99. The baseboard (9½) and picture-rail (103) heights were measured in the bedroom and carried over; check them once in living, dining and the hall (sheet M8).
- Chair rail in living and dining is owner-confirmed.
- Bedroom follows its October 12 packet plus Wall B Revision B (Urbane Bronze, twelve frames, three low dark outlets).
- Kitchen outlets follow Electrical Rev A (10 receptacles). Bathroom tile follows TP1-R3a.
- L01 living wall set-out is fully dimensioned (R2). Outlet positions on it are worked out below.

Open items, with owners

- **Tisa — one choice:** living/dining outlets at 18 in, white, centred inside the lower frames (current proposal), or the bedroom method (11½ in, horizontal plate under the frames). Everything below is drawn at 18 in.
- **Tisa — lock or reject:** hall and kitchen trim suggestions (marked New suggestion).
- **Electrical, decided by our crew:** no boxes inside door pockets (L6/D6 final spot waits for pier widths M4/M5; bathroom controls on the solid jamb side); dining outlets on their own 20 A small-appliance circuit; laundry keeps GFCI + AFCI protection. Rough-in still needs the city inspection before walls close.
- **Site tape, one pass:** the yellow fields on the Measure on site sheet. Not in Magicplan or any drawing found.

M Measure on site — fill in the yellow boxes

Only these numbers are missing; everything else comes from Magicplan and the existing drawings. Inches, to the nearest ⅛.

> **Measure the plain wall between the existing trim — do not include the trim.** Hold the tape about 36 in off the floor, above the baseboard. Only if a corner or casing is out of plumb, also measure at 90 in.

#	WALL	MEASURE	FROM	TO	AT 36 IN	AT 90 IN (IF NEEDED)
M1	D01 dining north	Plain wall width W	inside corner (or casing outside edge)	other corner (or casing outside edge); leave out the transom doorway	_____ in	_____ in
M2	D04 dining west	Plain wall width W (subpanel wall)	outside edge of rightmost window casing	right inside corner	_____ in	_____ in
M3a	L03 fireplace	Plain wall, left of mantel	left inside corner	mantel side	_____ in	_____ in
M3b	L03	Plain wall, right of mantel	mantel side	right inside corner	_____ in	_____ in
M3c	L03	Mantel width / mantel height	mantel outer edges / floor	— / top of shelf	_____ in	_____ in
M4a	L02 living pocket face	Left pier	left inside corner	outside edge of door casing	_____ in	_____ in
M4b	L02	Right pier	outside edge of door casing	right inside corner	_____ in	_____ in
M4c	L02	One door leaf width	leaf edge	leaf edge	_____ in	_____ in
M5a	D03 dining pocket face	Left pier	left inside corner	outside edge of door casing	_____ in	_____ in
M5b	D03	Right pier	outside edge of door casing	right inside corner	_____ in	_____ in
M6	D02 dining south	Plain wall width W (move the buffet out first)	left inside corner (or casing outside edge)	right inside corner (or casing outside edge)	_____ in	_____ in
M7	all walls	Casing face width (door / window)	casing outside edge	casing inside edge	_____ in	_____ in
M8a	living (any wall)	Height: baseboard top / picture-rail underside	finished floor	top of baseboard / underside of picture rail	_____ in	_____ in


#	WALL	MEASURE	FROM	TO	AT 36 IN	AT 90 IN (IF NEEDED)
M8b	dining (any wall)	Height: baseboard top / picture-rail underside	finished floor	top of baseboard / underside of picture rail	_____ in	_____ in
M8c	hall (any wall)	Height: baseboard top / picture-rail underside	finished floor	top of baseboard / underside of picture rail	_____ in	_____ in
M9	hall	Each plain wall piece between door casings (list them all, going around the hall)	casing outside edge or corner	next casing outside edge or corner	_____ in	_____ in

Measured by Date Photo of tape on each wall sent

Yellow = a field to fill in. The drawings below mark the same fields in yellow.

0 One trim system for the whole unit

Every paneled room uses the same heights, so lines carry through doorways. Rooms differ only in colour and in how many frames fit.

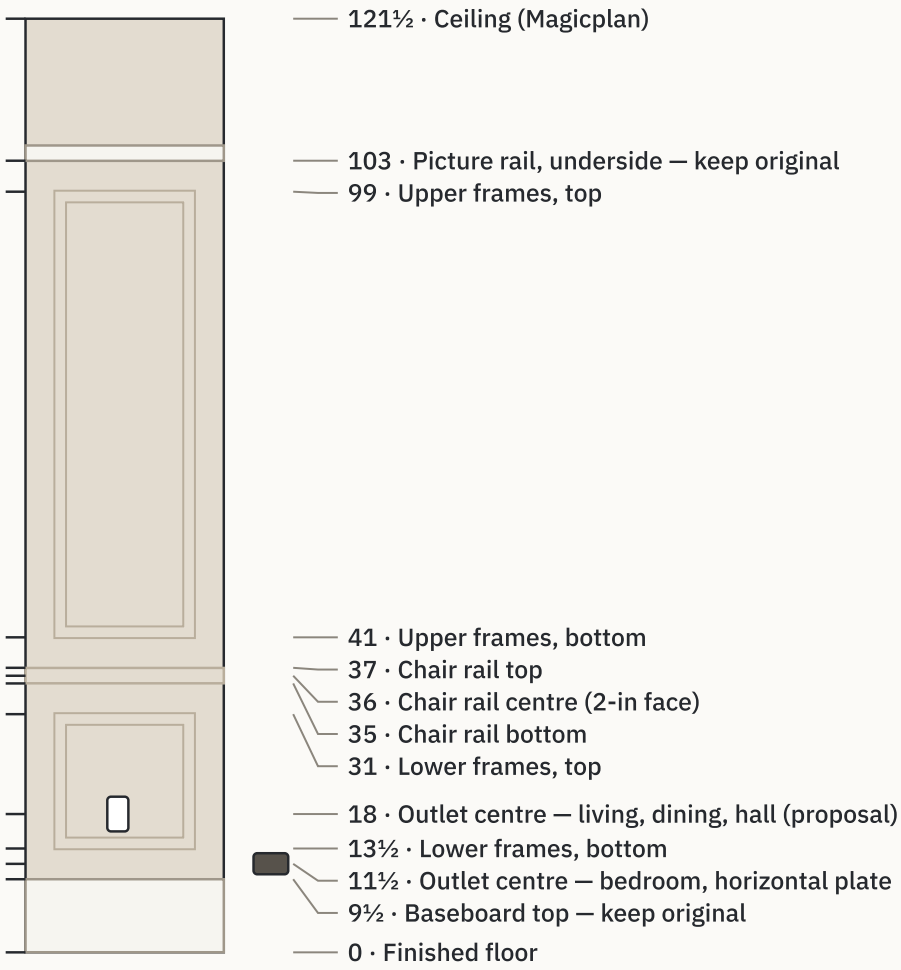

ELEMENT	SPEC	STATUS
Picture-frame moulding	House of Fara 719, 1¼ face, 11/32 thick; one outline per frame	Issued packet
Chair rail	2-in face, centre 36; stops at casings, cabinet, mantel	Owner-confirmed
Baseboard	Original — keep; no outlet boxes in it. Top at 9½ measured in the bedroom; living, dining and hall heights assumed the same until M8.	Issued packet Field check
Picture rail	Original — keep; no crown. Underside 103 measured in the bedroom; living, dining and hall assumed the same until M8.	Issued packet Field check
Living / dining paint	Walls, ceilings, new frames and chair rail: Pale Oak OC-20. Original woodwork: Chantilly Lace OC-65.	Working proposal
Bedroom paint	Urbane Bronze — eggshell walls, satin trim, flat ceiling	Issued packet
Frame rule	4-in margins and gaps; inner opening = outside size − 2½	Working proposal
Outlet rule	No trim crosses a plate. Switches stay outside frames. Outlets sit fully inside a lower-frame opening, never in a 4-in gap.	Working proposal

Why not in a 4-in gap: a standard plate is 2¾ wide, leaving under ⅝ in each side — it reads as a mistake. Inside a lower frame at 18 in, the plate (15¾–20¼) clears the frame's inner edge (14¾) by 1 in.

Colour swatches in the drawings are screen approximations, not paint matches.

1 Living room

Two-tier picture frames on three walls in Pale Oak, original woodwork in Chantilly Lace. Magicplan: 209 × 142 9/16, ceiling 121½.



L01 · IMG_0325




L03 · IMG_0327



L02 · IMG_0326

Walls

L01 · plain wall shared with bedroom Working proposal exact R2 set-out

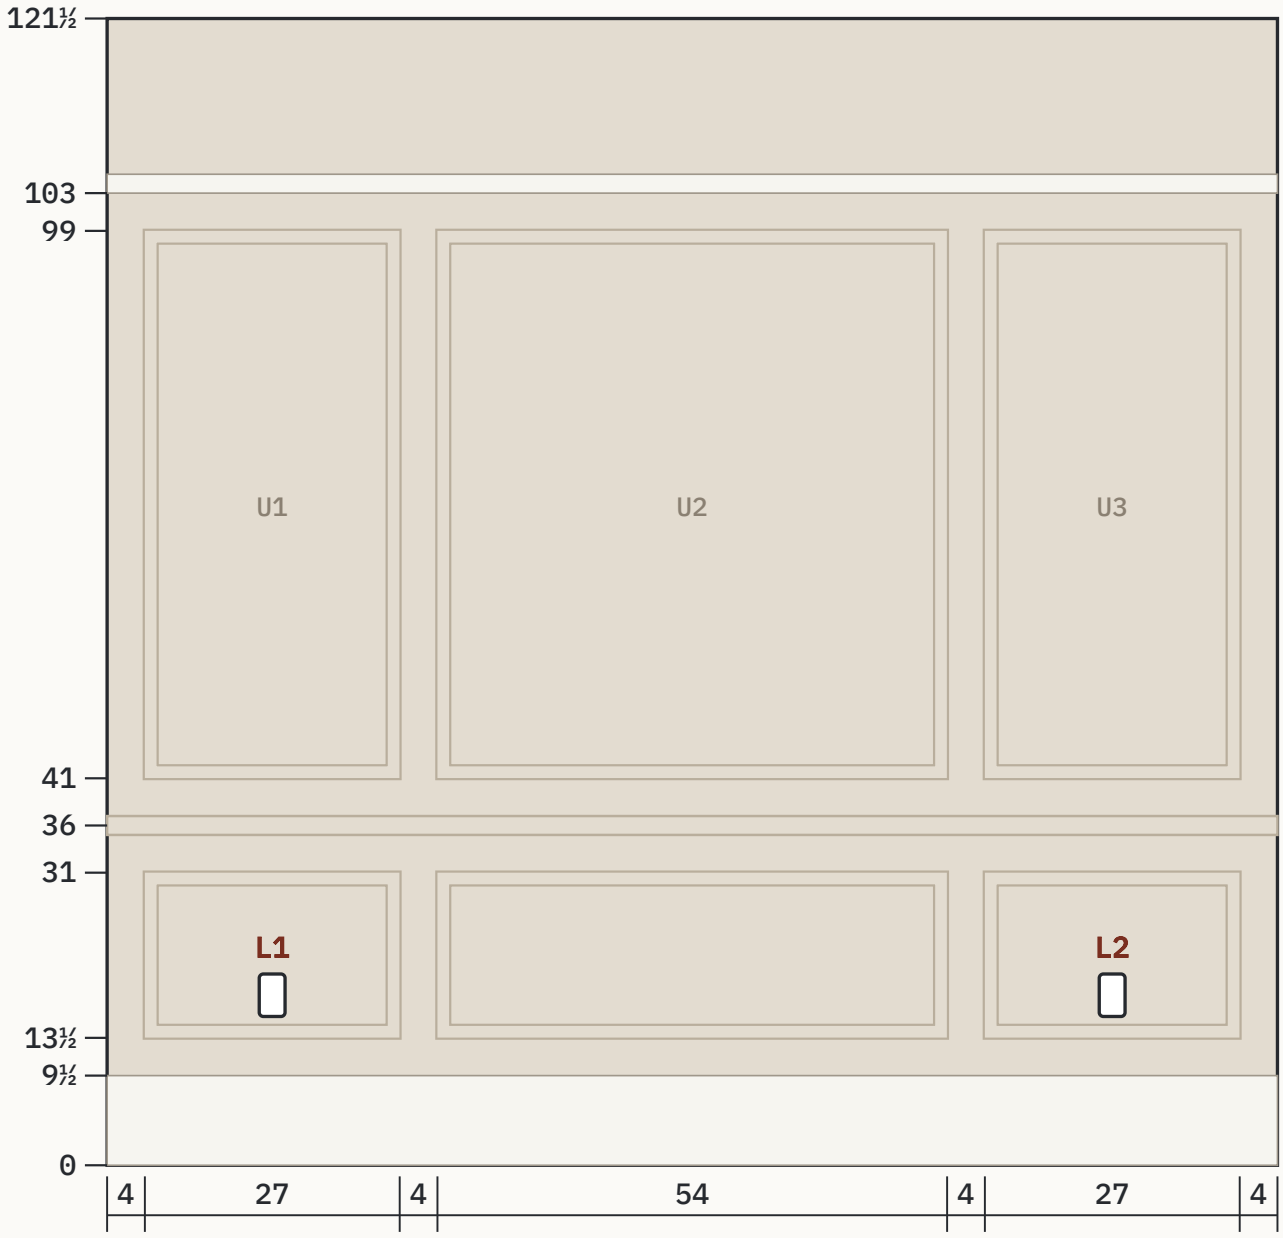


124 clear wall (R2) — confirm on site


FRAME	X	Y	OUTSIDE W × H	OPENING (1¼ FACE)
U1	4–31	41–99	27 × 58	24½ × 55½
U2	35–89	41–99	54 × 58	51½ × 55½
U3	93–120	41–99	27 × 58	24½ × 55½
Lower 1	4–31	13½–31	27 × 17½	24½ × 15
Lower 2	35–89	13½–31	54 × 17½	51½ × 15
Lower 3	93–120	13½–31	27 × 17½	24½ × 15

Check: 4 + 27 + 4 + 54 + 4 + 27 + 4 = 124. Frame moulding on this wall: 885 in of outside perimeter ≈ 74 ft before waste. x = 0 is the confirmed left end of the 124-in clear wall.

L03 · south fireplace wall Working proposal five frames; mantel and services hold

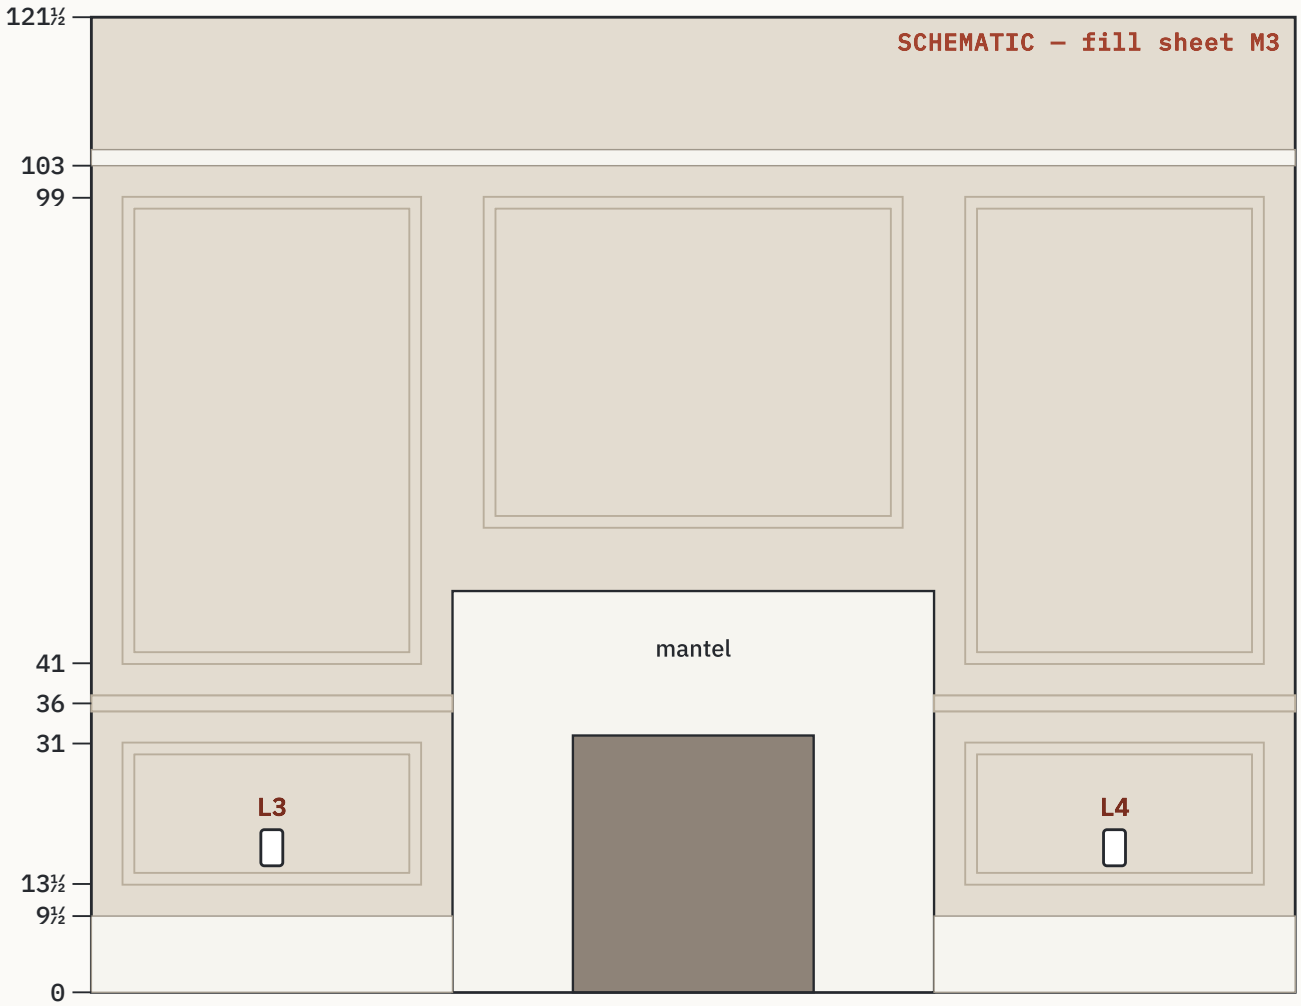

L02 · door-side pocket wall Electrical — decided L6 cannot sit in the pocket

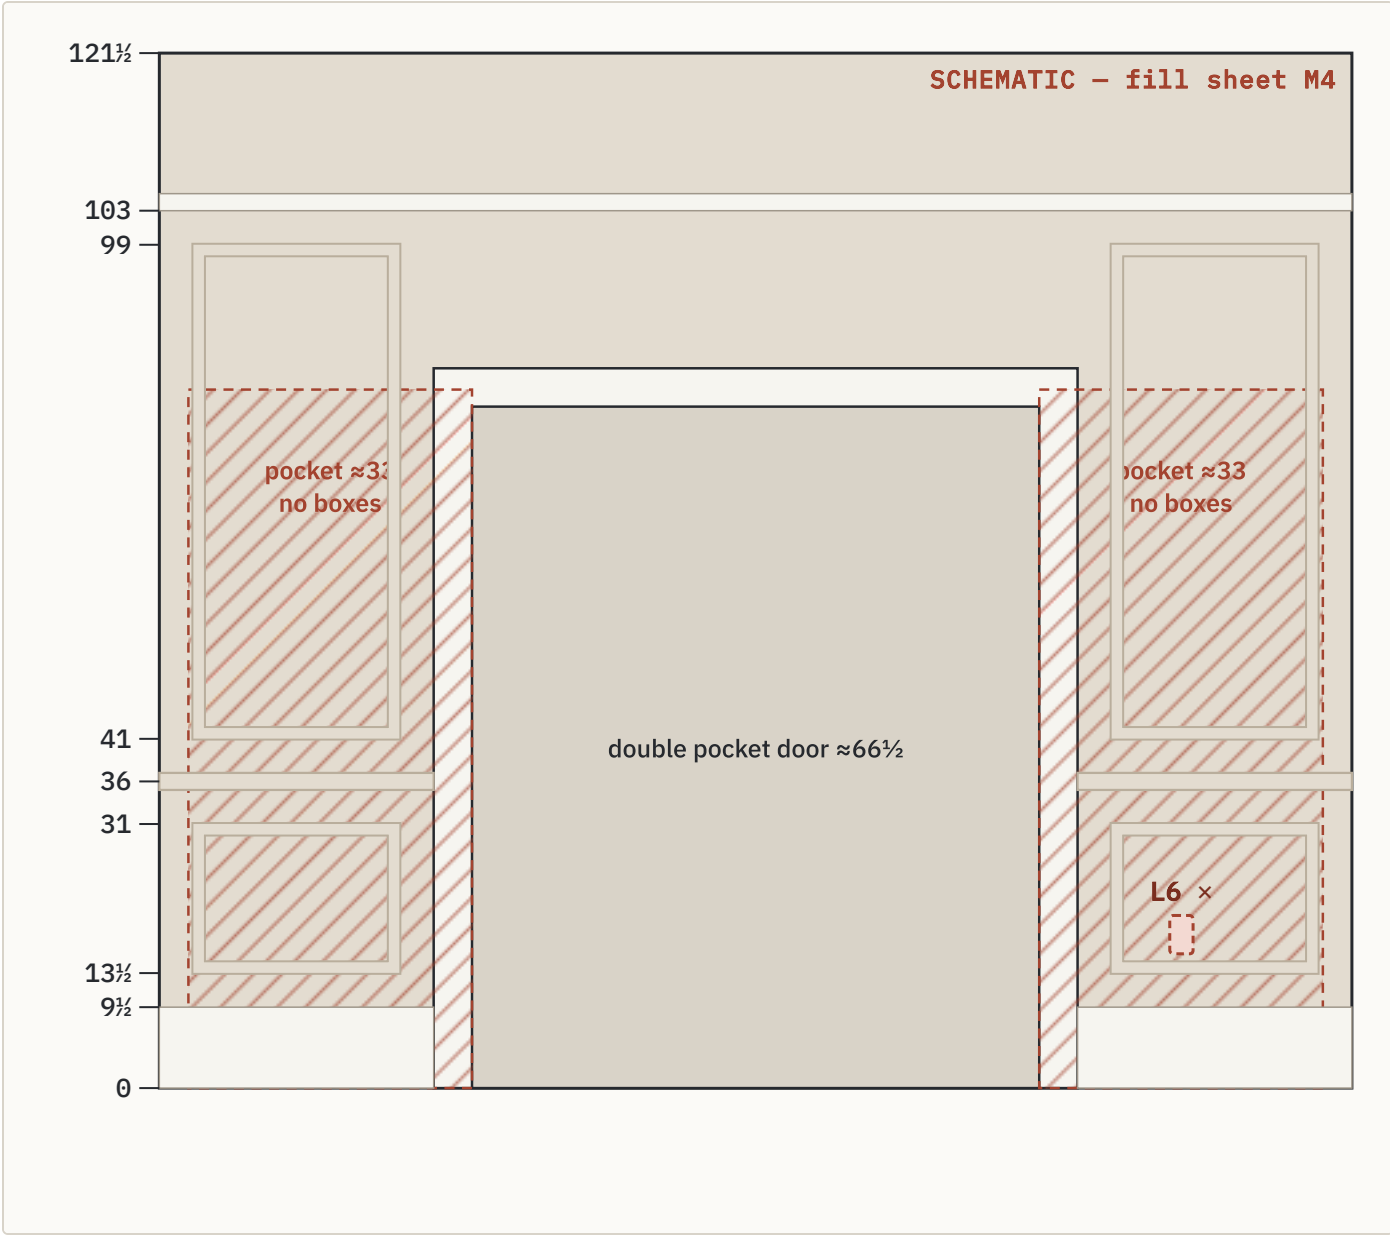

Outlets and usability

ID	WHERE	POSITION	USE	STATUS
L1	L01	x 17½, 18 AFF — centred in lower frame 1	lamp / end table	Working proposal
L2	L01	x 106½, 18 AFF — centred in lower frame 3	lamp / end table	Working proposal
L3 / L4	L03	centred in each side lower frame, 18 AFF	lamps beside the fireplace seating	Working proposal Field check
L5	L04 bay wall	not placed — wall never photographed straight on	keep below sill, outside curtain stack	Field check
L6	L02	move: only beyond the end of the pocket	see note	Electrical — decided

- **All living-room outlets are vertical** (Tisa, 2 Nov): standard upright white plate, 2¾ wide × 4½ tall, centred at 18 AFF inside the lower frame — plate spans 15¾–20¼. Owner-confirmed
- **Two outlets per wall, not three (Tisa, 2 Nov).** L01 gets only L1 and L2; the optional centre TV outlet is dropped. Coverage still passes: the farthest point from an outlet is 44½ in, inside the 6-ft rule.
- **Pocket piers (L6):** each leaf of the ≈66½-in double pocket door is ≈33 in, so roughly 33 in of wall beside each opening is hollow pocket. A box fits only past that. If the pier is under ≈37 in wide, drop L6 and let L1 cover that corner.
- **Fireplace wall:** no TV above the mantel in this plan (heat, viewing height). L3/L4 serve side-table lamps; the pipe/conduit strip in IMG_0453 must be resolved before any box or frame fixing.
- **Frames on pocket piers:** fix with adhesive and short brads only — nothing that could reach the pocket or the door track.
- **Switch by the L01 door:** stays where it is, outside U1 and lower frame 1.

2 Dining room

Two equal bays on every solid wall, movable buffet, subpanel behind art on D04. Magicplan: 146 11/16 × 155¾.




D01 · IMG_0300



D02 · IMG_0304




D03 · IMG_0336

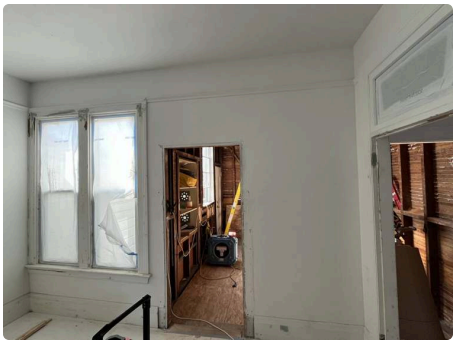


D04 · IMG_0328

Walls


D01 · north main wall Working proposal formula — W not yet measured

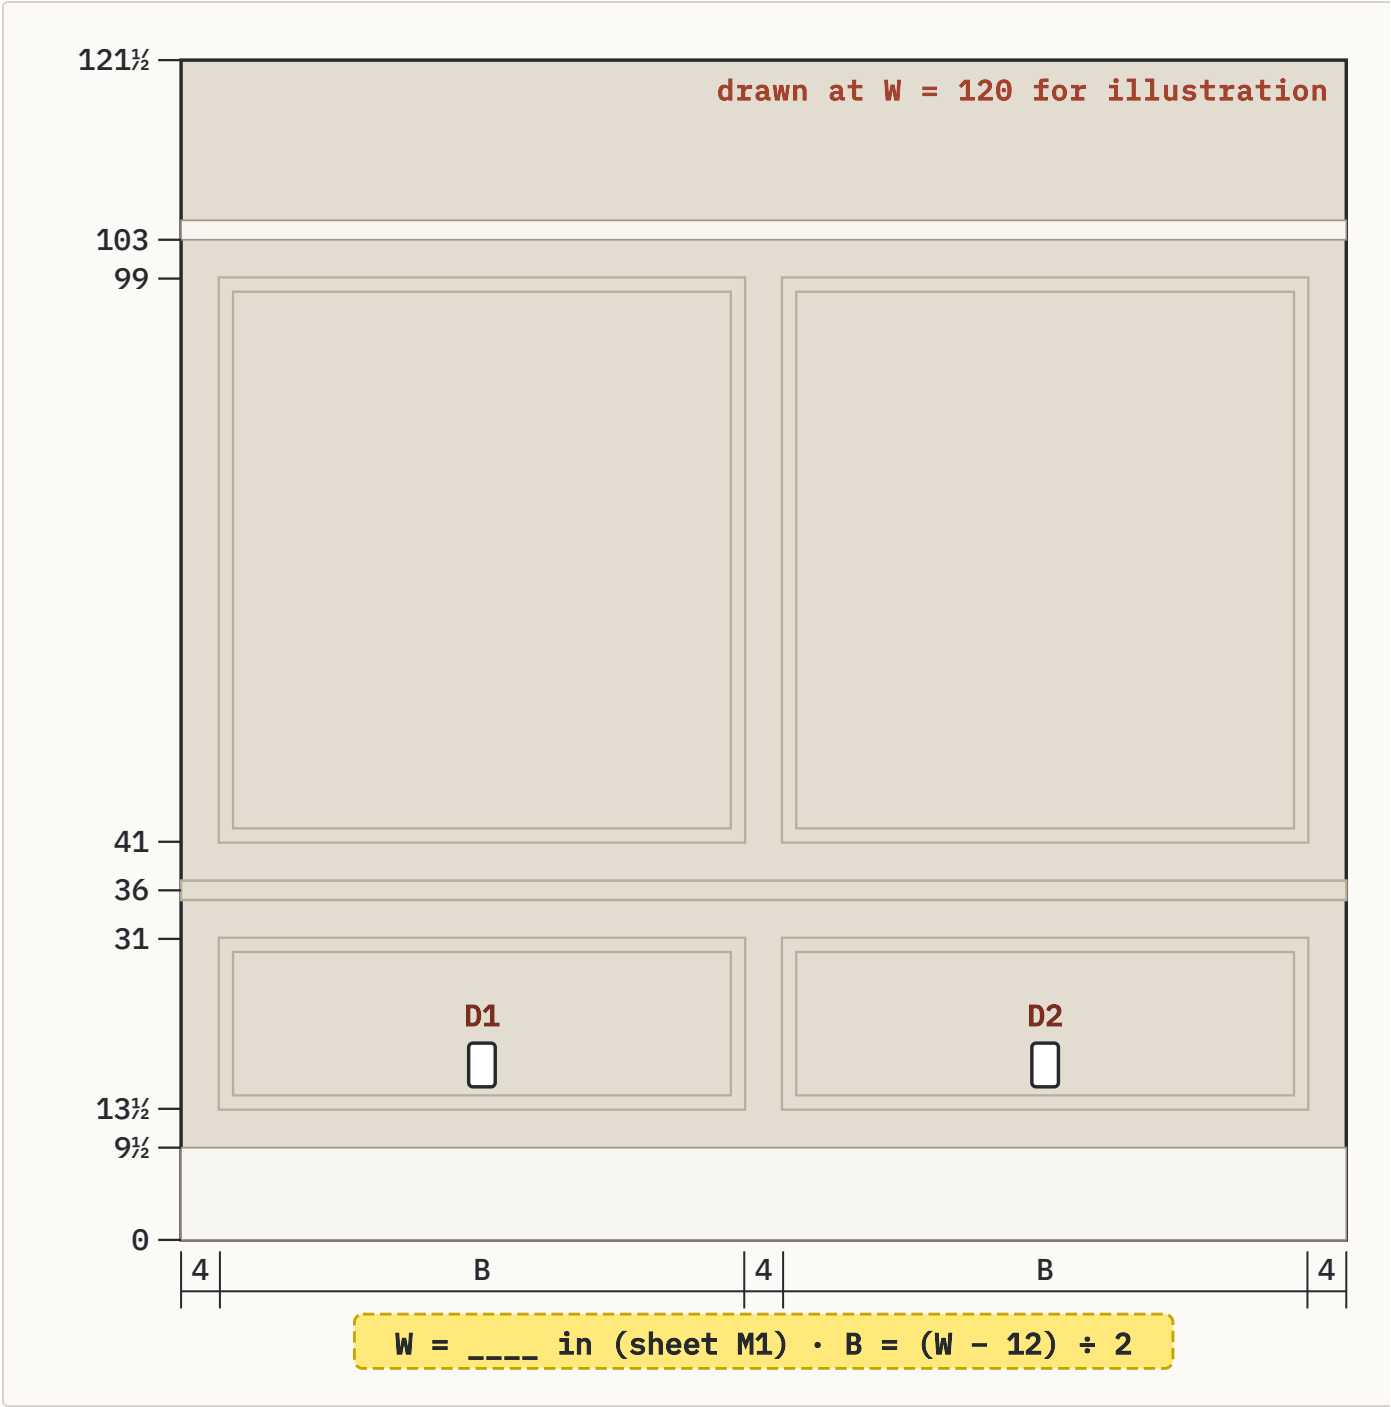


D02 · south wall — freestanding buffet New suggestion two equal bays, same rule as D01 and D04

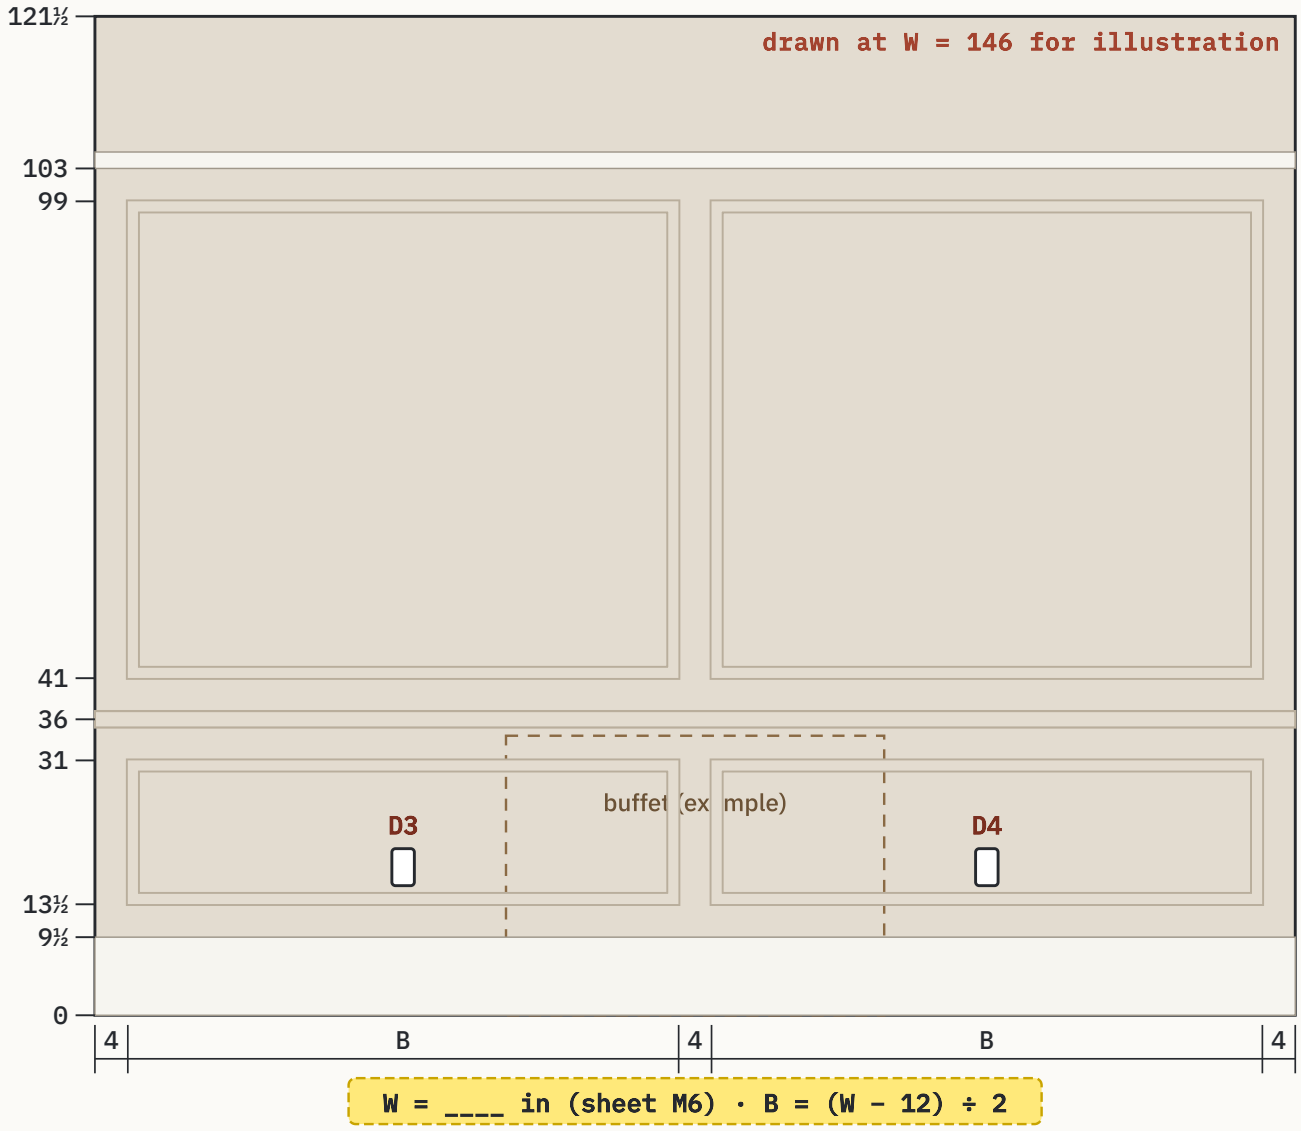

D03 · east pocket face toward living Electrical — decided D6 cannot sit in the pocket

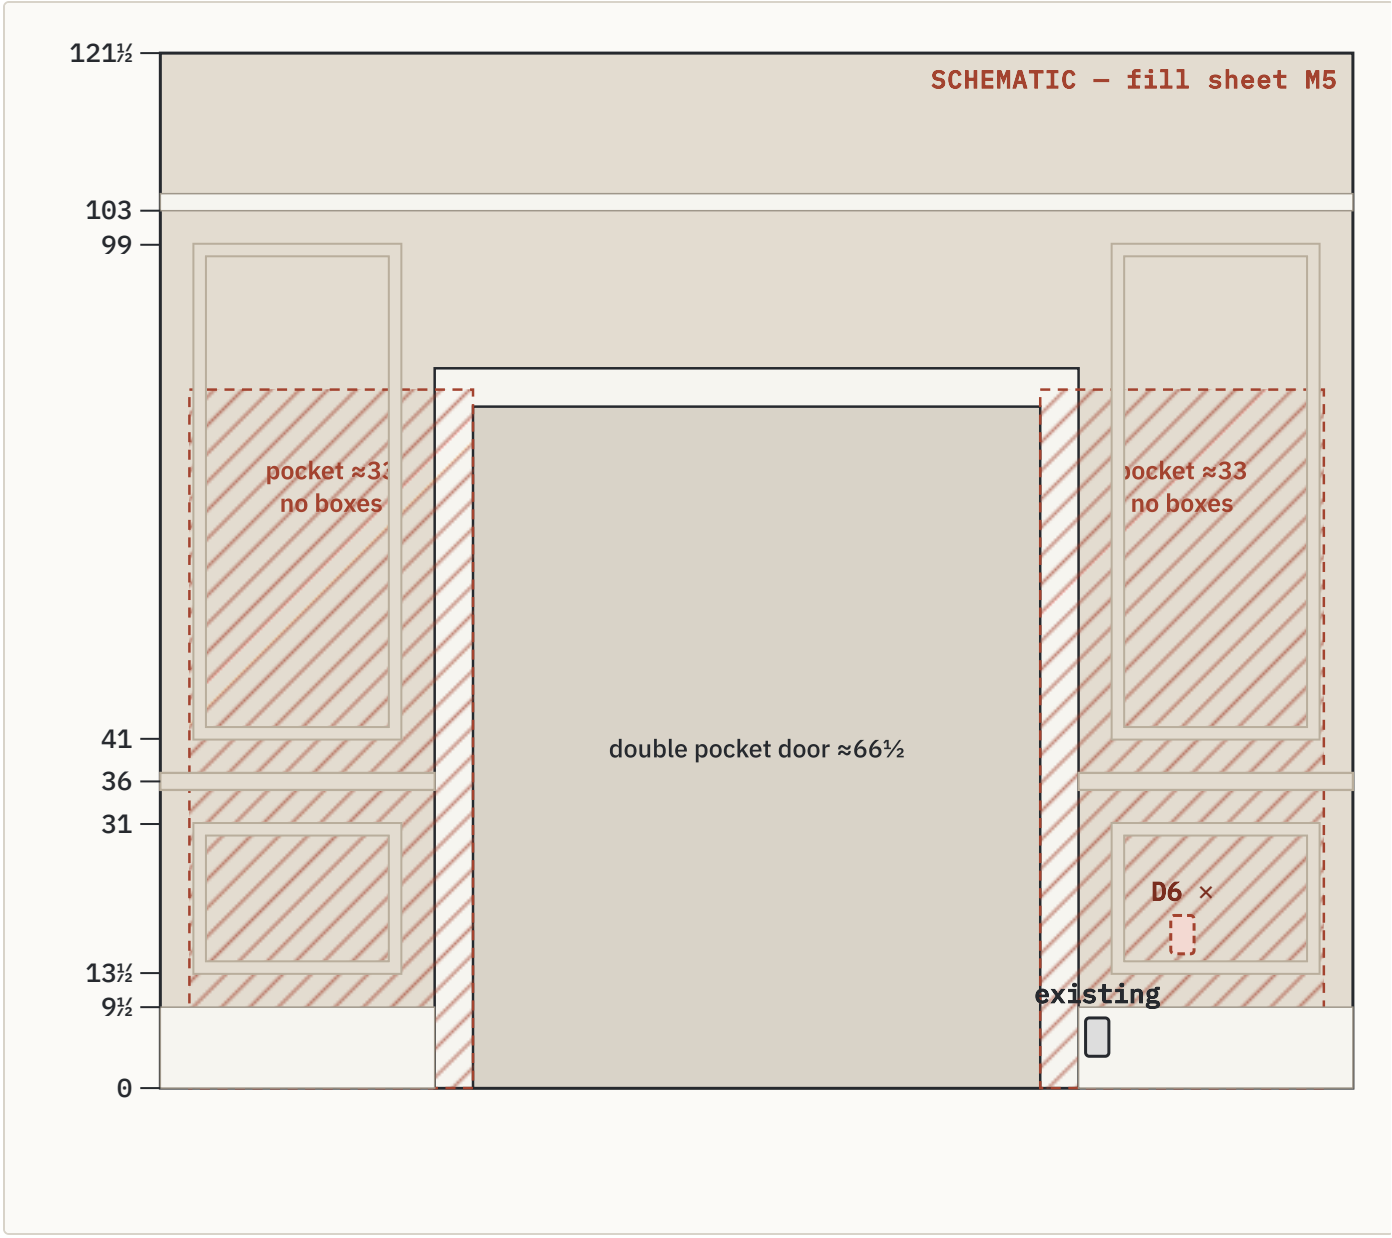

D04 · west window and infill wall — subpanel Working proposal panel centre x = W/4 + 1, 65 AFF

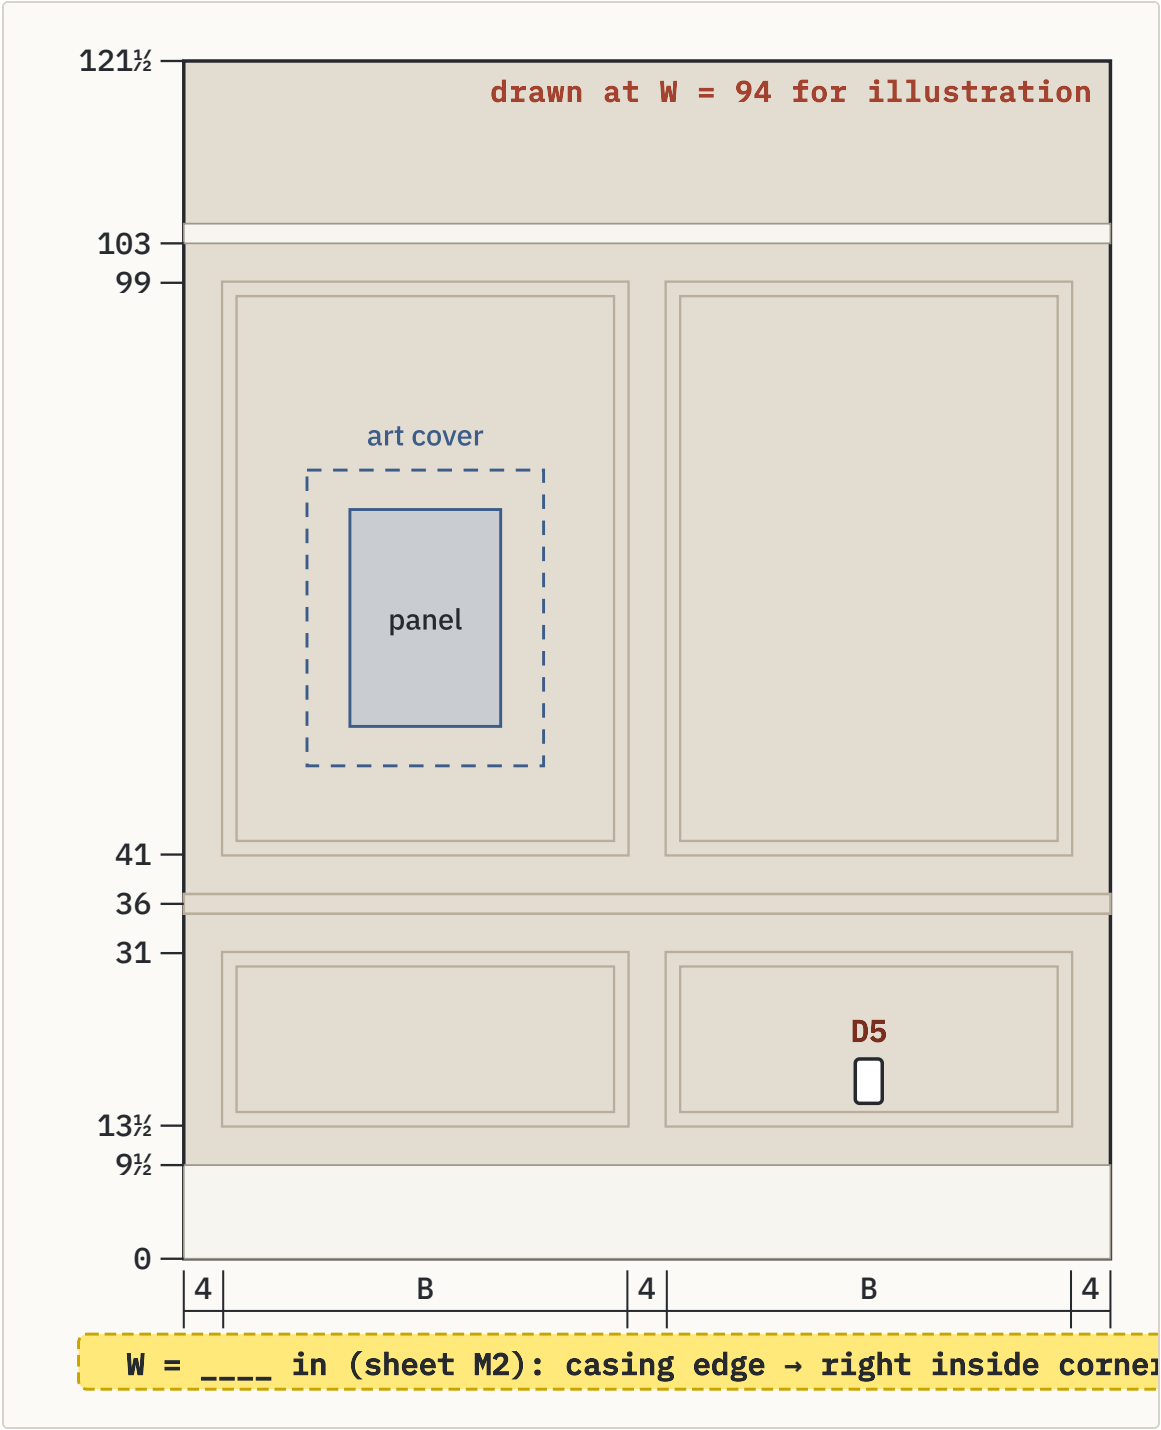

QUANTITY	FORMULA (D01, D02 AND D04, EACH MEASURED SEPARATELY)
Bay width B	(W – 12) ÷ 2
Left bay	x 4 → (W – 4) ÷ 2
Right bay	x (W + 4) ÷ 2 → W – 4
Left lower-frame centre (D1, panel)	(W + 4) ÷ 4 = W/4 + 1
Right lower-frame centre (D2, D5)	(3W – 4) ÷ 4
Example W = 94	B 41 · panel/D1 x 24½ · D5 x 69½


Outlets and usability

ID	WHERE	POSITION	USE	STATUS
D1 / D2	D01	centred in each lower frame, 18 AFF	vacuum, lamp, sideboard	Working proposal
D3 / D4	D02	centred in each lower frame, (W + 4) ÷ 4 and (3W – 4) ÷ 4, 18 AFF	buffet serving (coffee, warming tray)	Working proposal
D5	D04	right lower frame centre, (3W – 4) ÷ 4, 18 AFF	keeps the panel bay clean	New suggestion
D6	D03	move: only beyond the end of the pocket	existing low baseboard device stays a separate decision	Electrical — decided


- **D5 moved to the right bay (suggestion):** the subpanel and its art cover sit in the left upper bay. Putting D5 under the right bay keeps cords away from the panel's working space and the hinged cover.
- **Panel fit:** at W = 94 the left upper opening is 38½ × 55½; the BRPX2A20L1F cover (15.3 × 22) fits with room for an art cover. Final position waits for the can and cover in hand (D04 framing package).
- **Dining circuit, decided:** D1–D6 go on circuit 12 (DIN) as a **20 A small-appliance branch circuit**: 12 AWG, AFCI breaker, dining receptacles only — no lights and no other rooms on it. That is what the code asks of dining-room receptacles (NEC/CEC 210.52(B)), and it releases the whole-unit plan's hold on DIN. Electrical — decided
- **The dining buffet is freestanding and movable** (Tisa, 2 Nov; it has already been moved). So D02 no longer wraps a built-in: it gets the same two equal bays as D01 and D04, installed in full even where furniture stands in front, and D3/D4 sit in the two lower frames wherever the buffet ends up. R2's raised centre frame, headpiece and cabinet-return questions no longer apply. Owner-confirmed

3 Bedroom

Planned in its own packet; Wall B revised 2 Nov (Rev B). Summary and outlet check only.

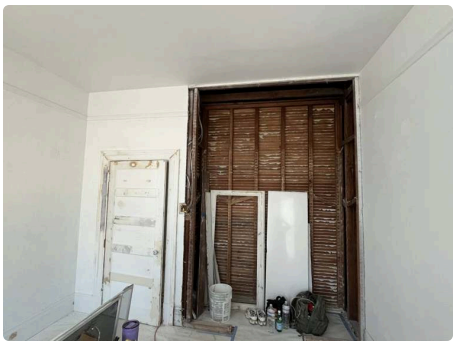

Toward entry: door left, niche right

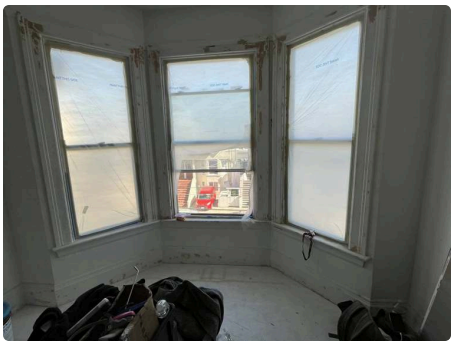

Bay windows




Wall A — headboard




Wall B — shared with living room

> The bedroom has its own plan: **Unit 4 Bedroom — Complete English Packet, 12 Oct 2026**, plus **Wall B Revision B (2 Nov 2026)**, which Tisa chose: three equal tall bays on Wall B. Wall A is unchanged. The drawings below repeat those numbers; the packet and Rev B govern.

Wall A · primary, beside the niche Issued packet six frames

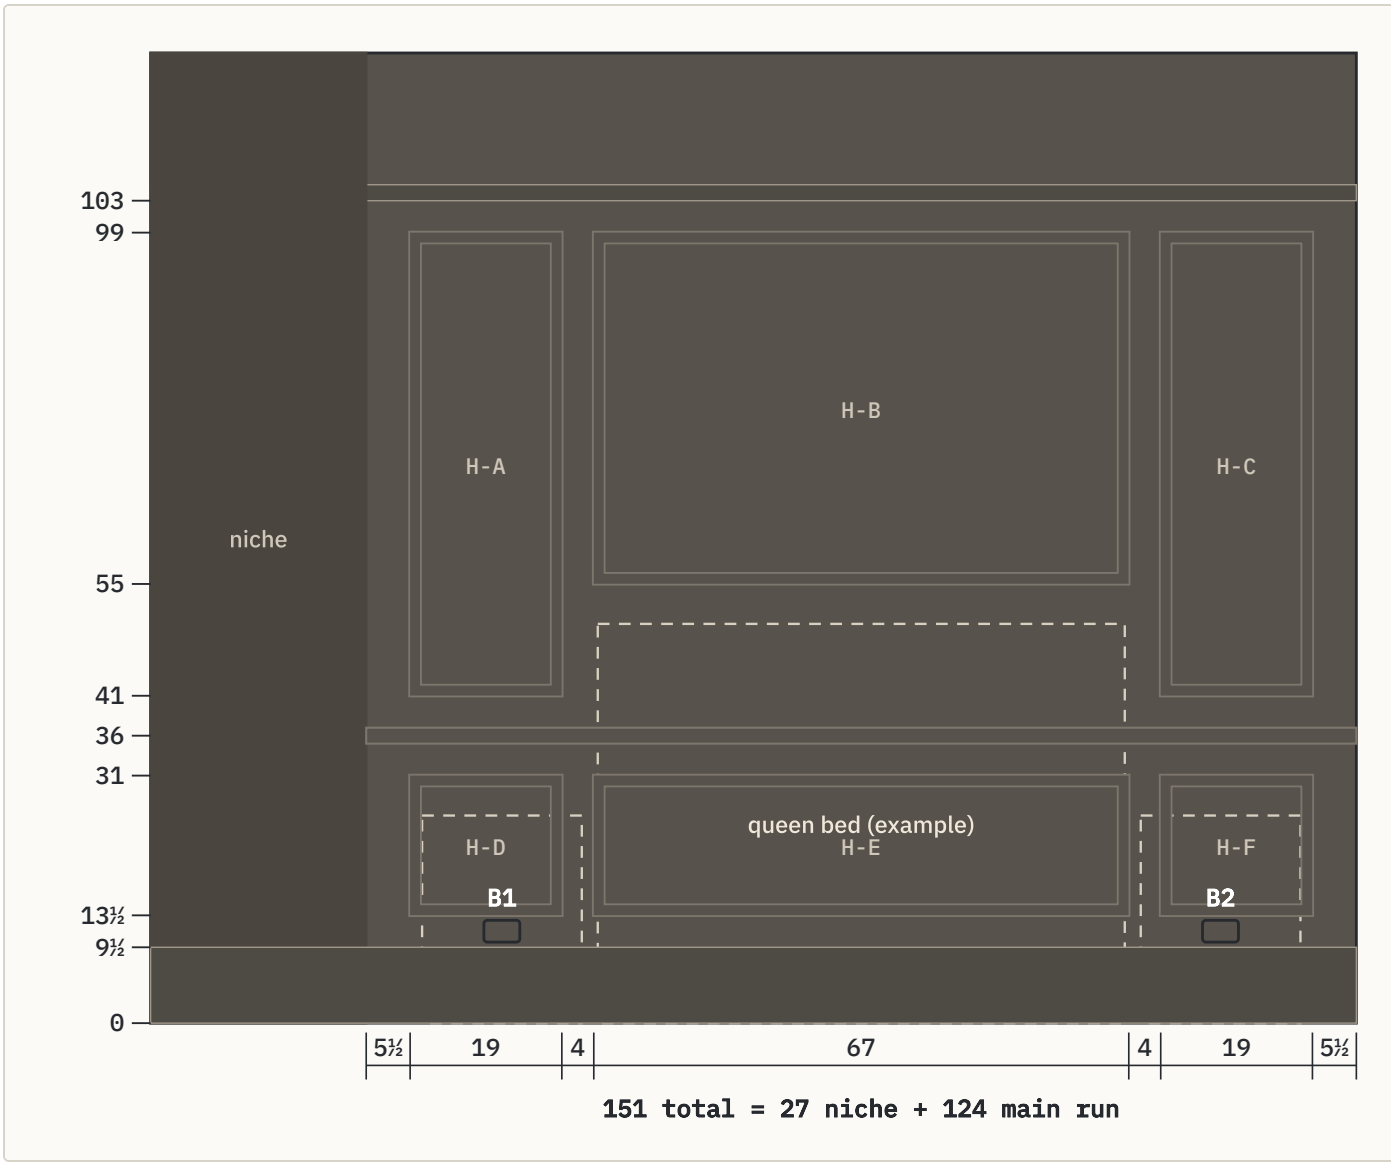

Wall B · shared with living room Owner-confirmed Rev B, 2 Nov — three equal tall bays, 31 / 43 / 31

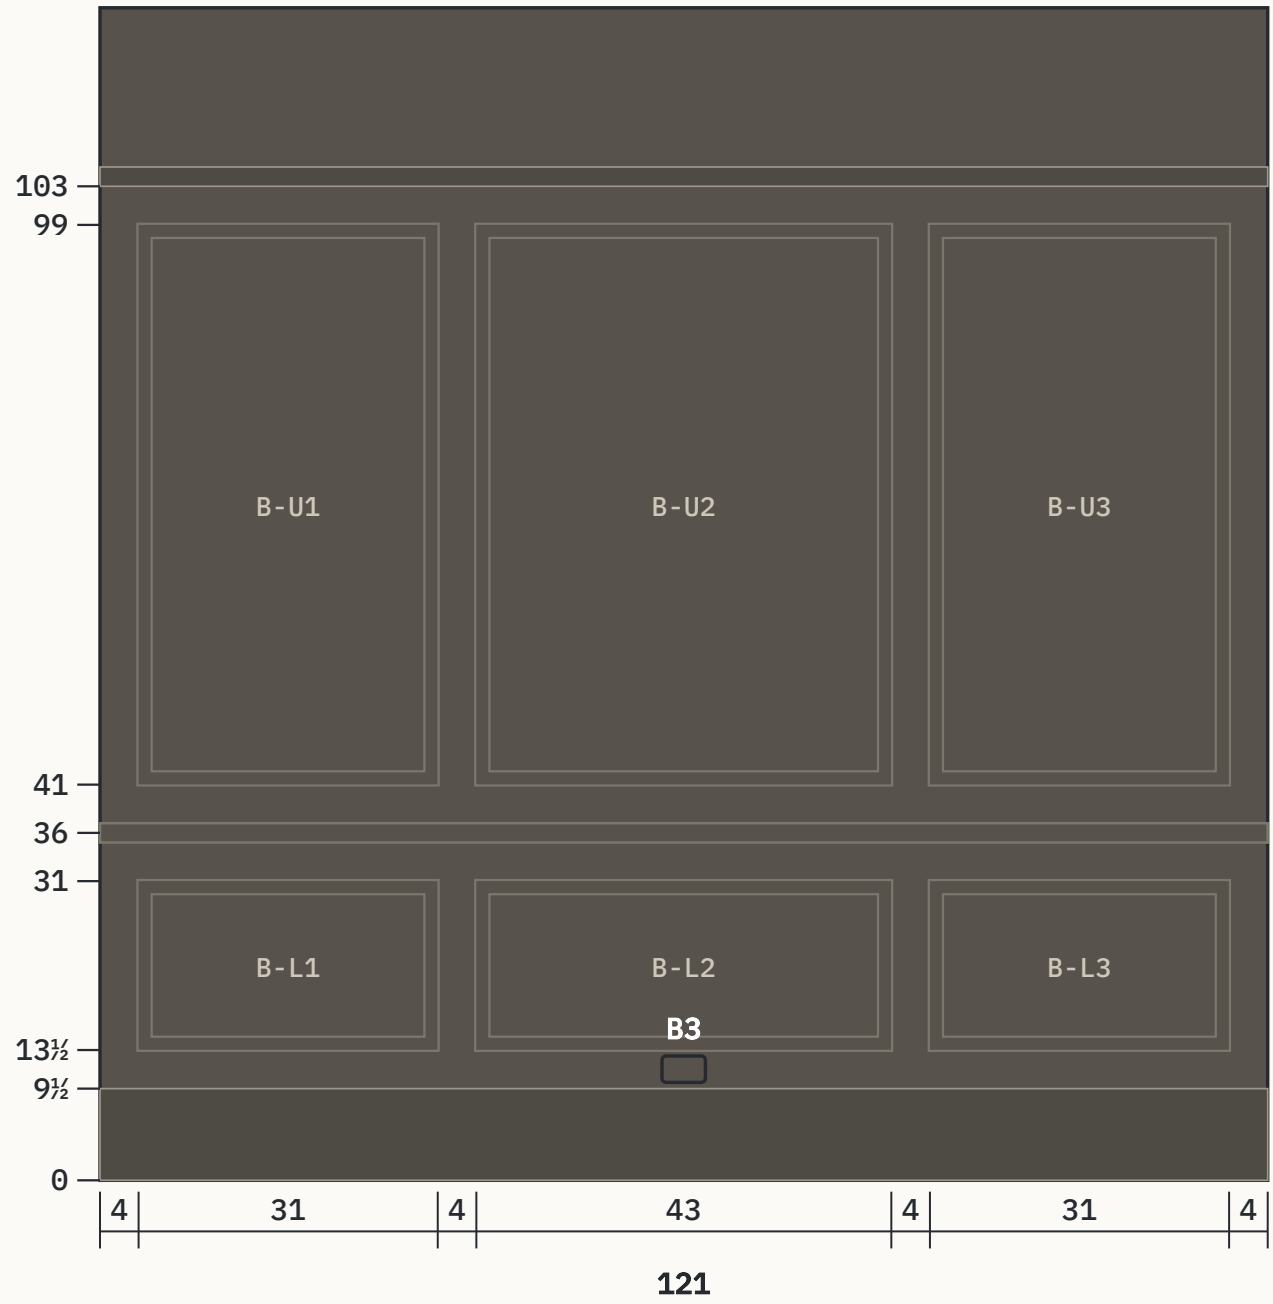

Outlet usability check against the packet

- **Bedside reach passes.** With the packet's example queen bed centred at 62, the side tables span 7–27 and 97–117. B1 (17) and B2 (107) land at the centre of each table — reachable, not hidden behind the headboard.
- **Plate fit passes.** A horizontal plate at 11½ spans 10⅛–12⅞, clearing the baseboard (9½) and frame bottoms (13½) by ⅝ in each.
- **Coverage passes** on A (17 in to each end of the run, 90 in between) and B (60½ to each end).

- **Count differs between sources:** the packet places 3 outlets; the Oct 27 whole-unit plan budgets 5 (adds a desk spot and a bay-wall spot). If the extra two are kept, use the same dark horizontal plate at 11½.
- **Device colour:** the bedroom uses dark devices and covers (packet). The whole-unit plan's white devices apply outside the bedroom.

4 Kitchen

Outlets locked by Electrical Rev A; wall finish is the open decision. Magicplan: 147 × 126¼, ceiling 121½.



IMG_0321



Toward hall and old doorway




Range wall side


Walls

- Walls are open to lath; new drywall throughout. No picture frames or chair rail — cabinets, counter and backsplash take the wall. New suggestion
- Paint the kitchen walls and ceiling Pale Oak and the hall-opening casing Chantilly Lace, so the kitchen reads as part of the dining/living colour set through the openings. Cabinet colour stays its own decision (Essex Green was the earlier direction). New suggestion
- Backsplash material is still TBD. Boxes in the tile zone use 4-in square boxes with mud rings sized to tile + setting bed (Rev A E-11).


South wall · sink run Issued for bid Rev A E-7

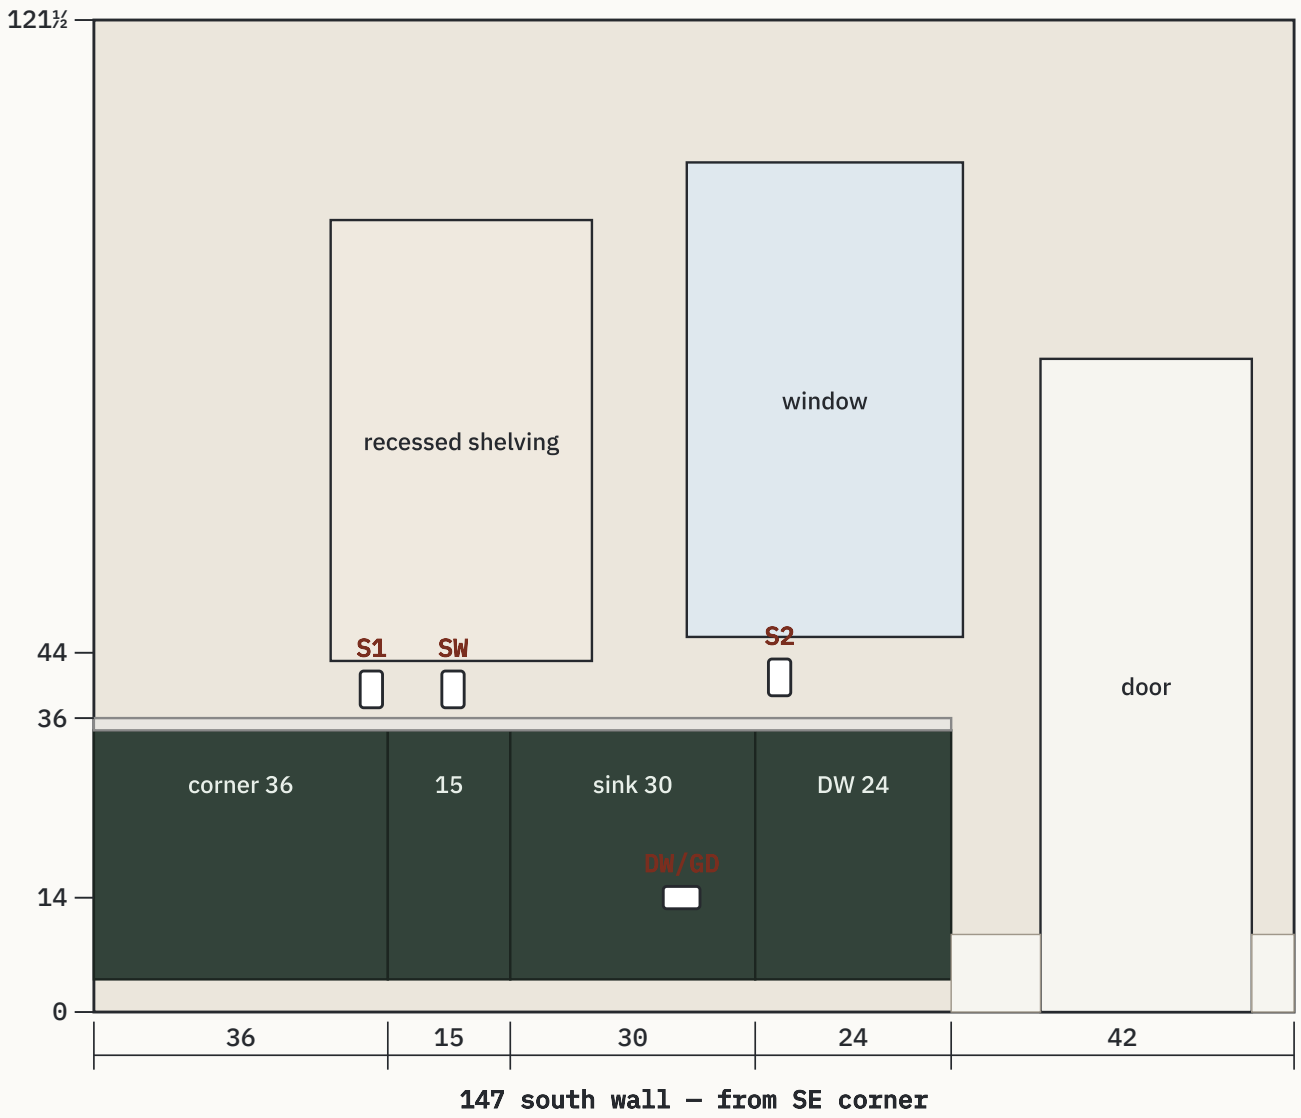

East wall · refrigerator run Issued for bid Rev A E-8

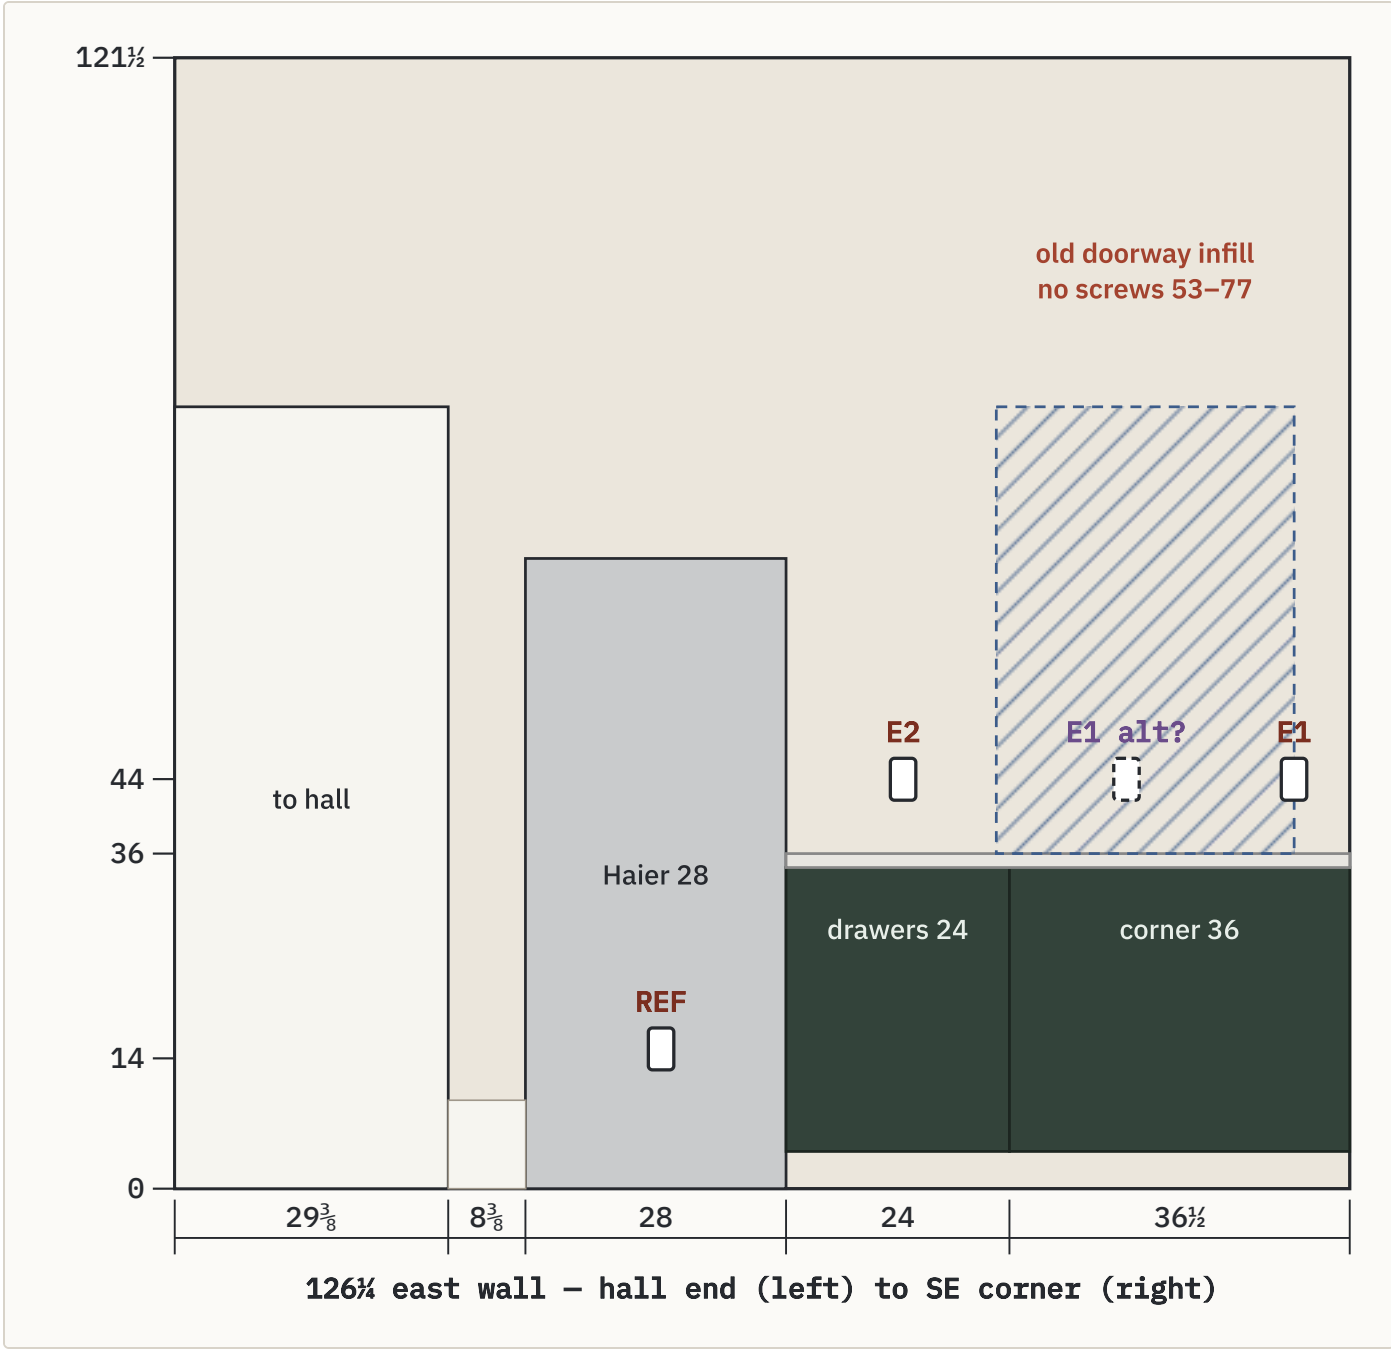

West wall · range Issued for bid Rev A E-9

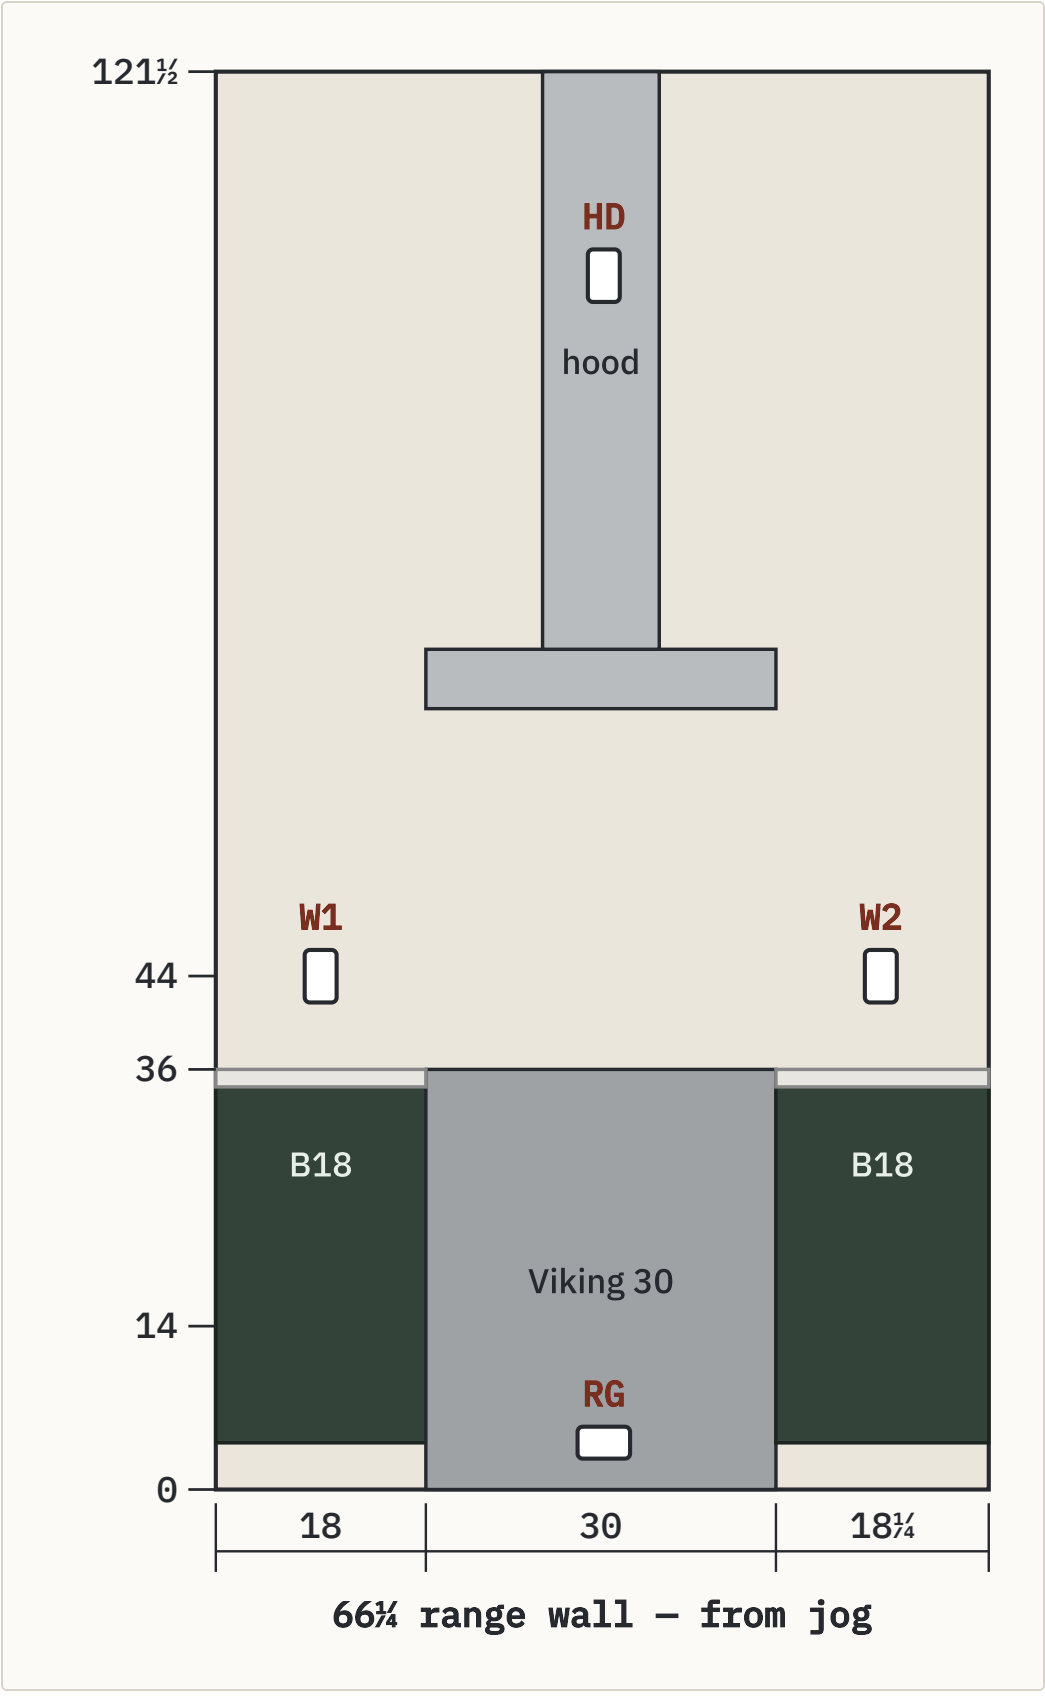

Usability review of Rev A (no changes made)

- **E1 is deep in the blind corner.** At 6 in from the SE corner it sits behind a 36-in corner cabinet, about 25 in back and hard to reach. Moving it to about 24 in north (dashed “E1 alt?”) still covers the corner

and keeps E1–E2 spacing at 24 in. Only if Tisa agrees. New suggestion


- **No microwave home.** Rev A has no microwave location. Countertop on the east drawer counter works on E2; a microwave drawer would need its own circuit. New suggestion
- **Subpanel location changed after Rev A.** Rev A says “accessed from the living room”; the current lock is D04, facing dining, in the old doorway infill (s ≈ 6–38 from the SE corner). E1 must not route through the can bay; kitchen face over the bay has a no-screw zone 53–77 AFF. Electrical — decided
- **Furnace note:** Rev A lists Lennox; the current HVAC basis is Trane S8X1A040M3PTCC. Circuit 10 stays, model reference updates.
- Counter receptacles at 44 AFF sit 8 in above the 36-in counter — good for a tiled backsplash. Align plates to a tile course once the tile is chosen.

5 Hall


A connector with seven openings. Three trim options to choose from, with a materials estimate. Magicplan: 205 7/16 × 95 15/16.



Looking down the hall

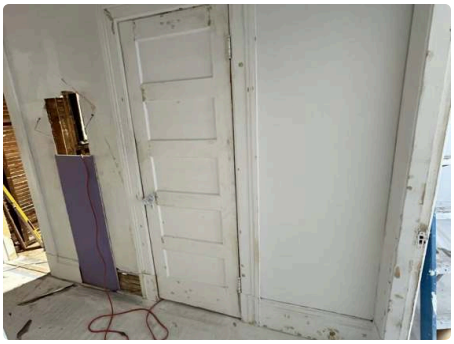

Middle hall door (Murphy location)

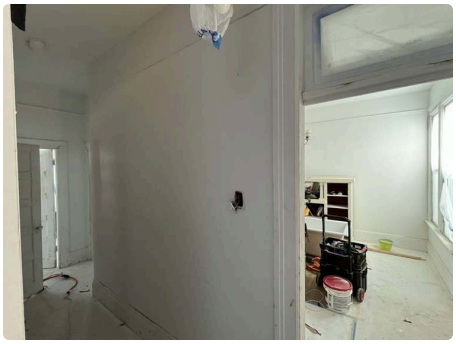


IMG_0329


Wall treatment — three options

The hall has seven openings, so its wall comes in short pieces between door casings. Each option below is drawn on a typical 61-in piece. Rule for all options: frames go only on pieces at least 24 in wide between casings; narrower pieces get the chair rail alone. Nothing is mounted on the Murphy bookcase door or inside its swing.


A · Chair rail only New suggestion

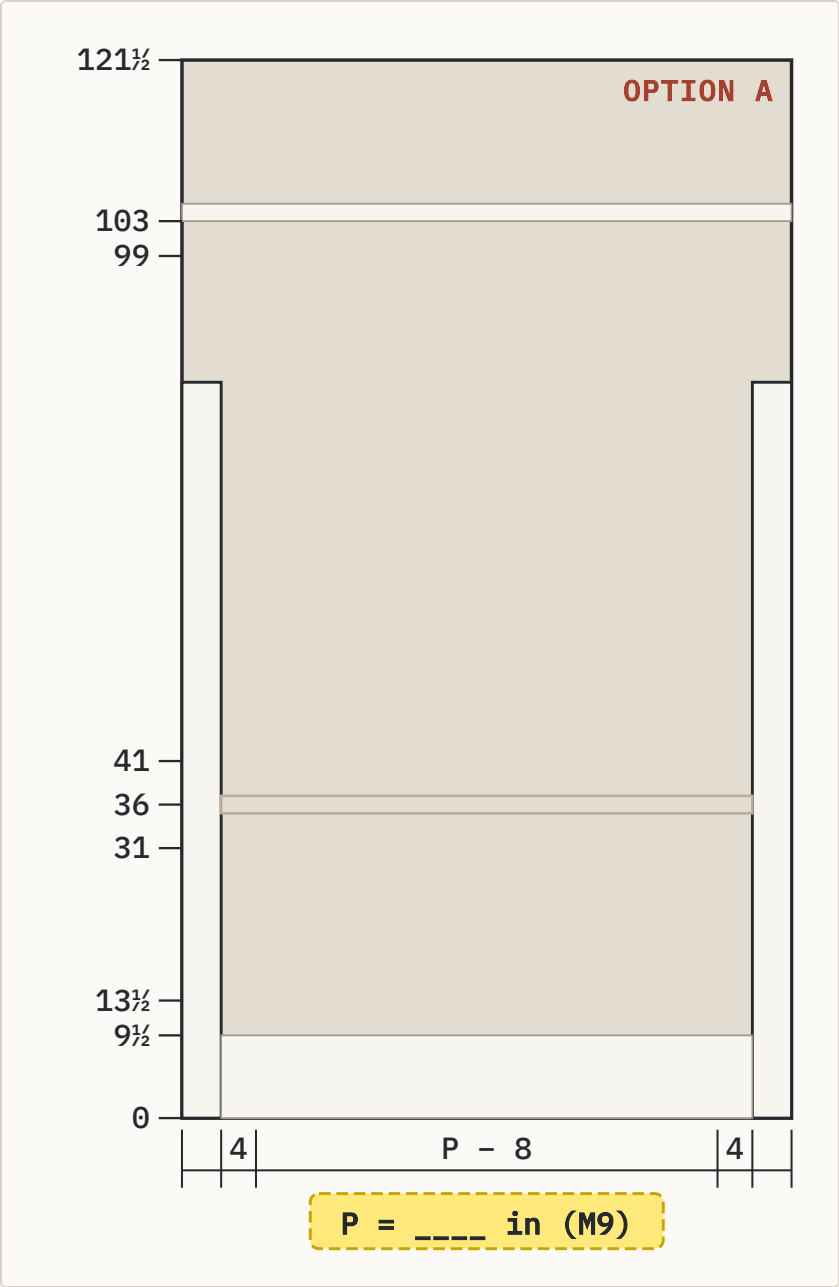

B · Chair rail + lower frames New suggestion

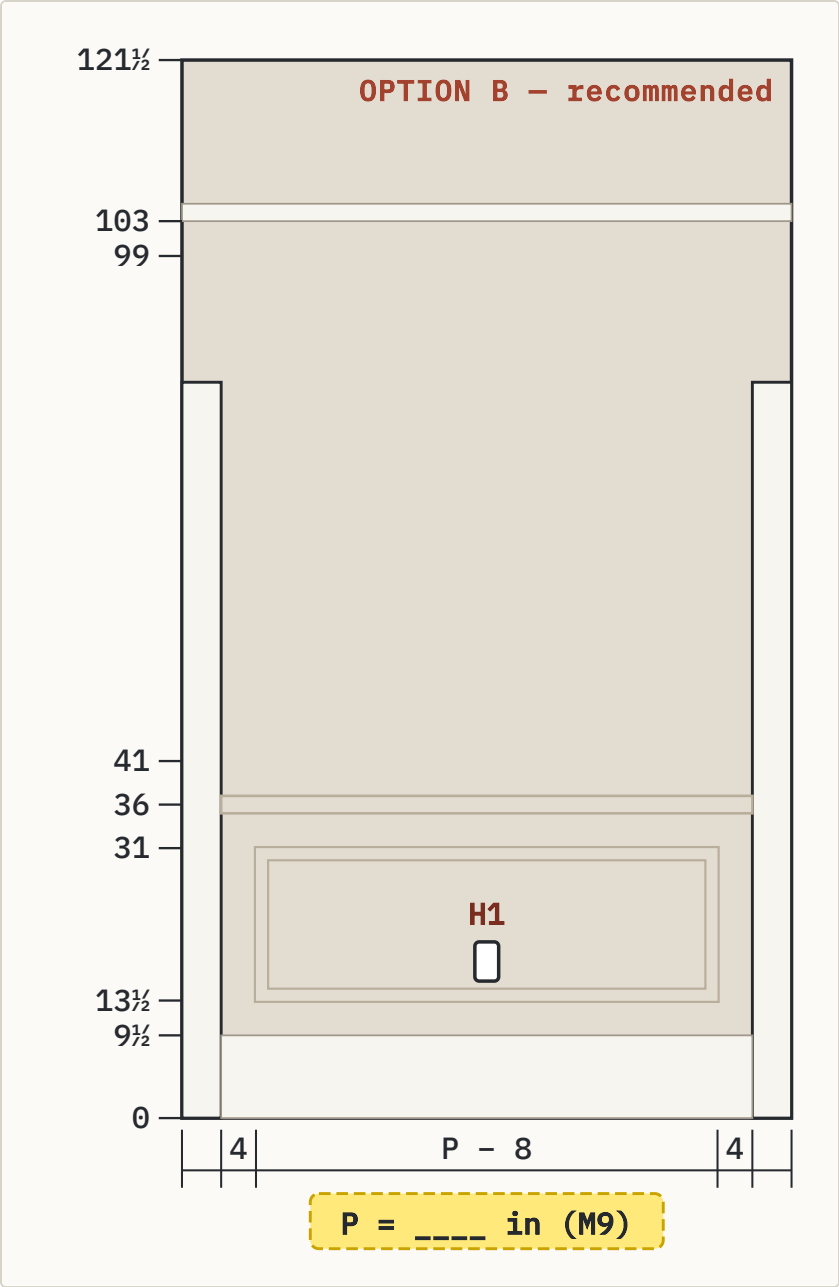

C · Full two-tier frames New suggestion

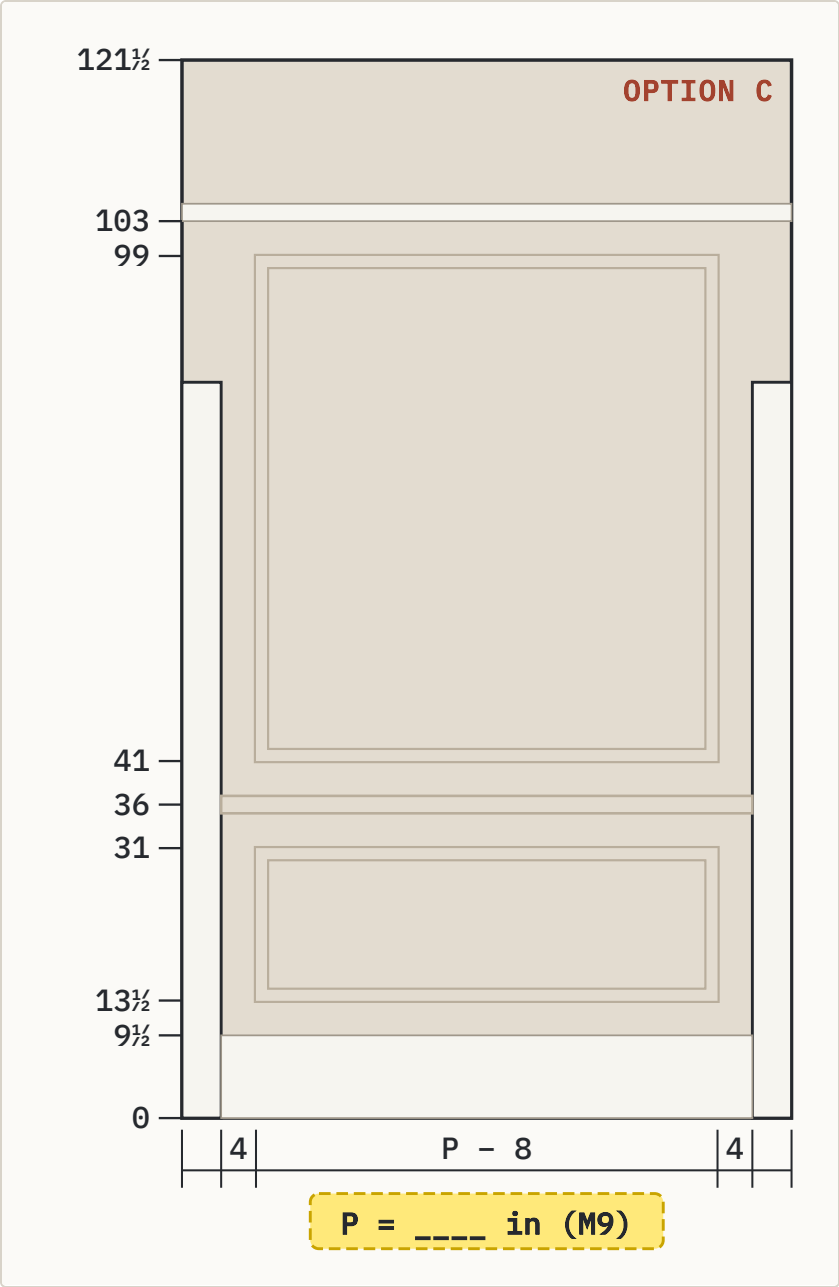

- **A — chair rail only:** carries the living/dining line through the hall at 35–37, stopping at every casing. Quietest and cheapest.
- **B — chair rail + one lower frame per wall piece (recommended):** 13½–31, 4-in margins, same as the lower band in every other room. Reads as a panelled wainscot, hides scuffs where a hallway takes wear, and keeps the upper wall calm next to seven doors. H1 sits centred in one lower frame.
- **C — full two-tier:** adds upper frames 41–99 on each piece. Richest, but with doors every few feet it can look busy; best only if most pieces are 36 in or wider.

All options: walls and ceiling Pale Oak OC-20; original casings, doors, baseboard and picture rail kept in Chantilly Lace OC-65; new chair rail and frames Pale Oak, tonal with the walls, same House of Fara 719 profile as the other rooms. New suggestion

Estimated materials — hall

From Magicplan: hall perimeter about 603 in, seven openings totalling about 224 in plus casings, one window. That leaves roughly 275 in (≈ 23 ft) of plain wall at chair-rail height, assumed here as about six pieces. Replace with the measured pieces from sheet M9 before ordering.

ITEM	A	B	C	BASIS
Chair rail, 2-in face, 12 ft	3	3	3	23 ft + 15% waste; packet allowance ≈ $37.50 per 12-ft piece
House of Fara 719, 8 ft	—	9	22	B: 6 lower frames ≈ 55 ft; C: + 6 upper ≈ 151 ft total; 93 in usable per board + 1 spare; $10.28 each (12 Oct listing)
Loctite Power Grab, 9 oz	2	4	7	≈ 27.6 ft per tube, with the packet's allowance
DAP ALEX FLEX caulk	1	2	3	fine bead at wall edges
Brads 18 ga × 1¼, filler, primer	use bedroom stock	use bedroom stock	use bedroom stock	bedroom order covers these
Wall paint, Pale Oak, eggshell	2 gal	2 gal	2 gal	≈ 358 sq ft of wall (Magicplan), two coats at ≈ 350 sq ft/gal
Ceiling paint, Pale Oak, flat	1 gal	1 gal	1 gal	≈ 82 sq ft, two coats
Trim paint, Chantilly Lace, satin/semi-gloss	1 gal	1 gal	1 gal	7 door casings + doors, window, baseboard, picture rail
Moulding + adhesive + caulk, listed/allowance	**≈ $129**	**≈ $237**	**≈ $392**	before paint, tax and delivery; prices from the 12 Oct bedroom packet, not re-checked

Estimate only: no order placed and nothing bought without Tisa's approval. Wall pieces, opening count and casing widths come from Magicplan and photos, not a site survey.

Outlet

- **H1, one outlet, 18 AFF** on a solid wall piece, for vacuum and cleaning. A hall over 10 ft long needs at least one; this hall is about 17 ft. Working proposal
- Keep H1 out of the Murphy door's swing and the bedroom door's swing, and not on the bathroom pocket wall. The plain wall between the bathroom door and the Murphy door is the first place to check. Field check

6 Bathroom

Tile is settled in TP1-R3a; this section covers paint above tile and device placement only. Magicplan: 72⅛ × 82⅛.



Bathroom door from hall



IMG_0339

Wall treatment

SURFACE	PLAN	STATUS
Tiled walls	Daltile Restore Bright White 3×6 glossy RE1536MODHD1P4 + 2×6 bullnose, within the TP1-R3a tile stops (83 measured; 88½ conditional)	Owner-confirmed
Floor	STAINMASTER Calacatta Gem 12×24 matte + 3×12 bullnose	Owner-confirmed
Wall above tile and ceiling	Chantilly Lace in a bath-rated satin; keeps the white tile clean-looking	New suggestion
Door casing	Keep visible casing and opening appearance (PD-01 R4)	Owner-confirmed

Outlets, switches and usability

- **V1 vanity GFCI** within 36 in of the pedestal basin edge, beside the mirror at about 40–44 AFF so a hair dryer reaches the basin. Place it with the mirror and vanity light together. Working proposal
- **T1 toilet-side GFCI** for a possible bidet seat: low, beside the tank, clear of the tub zone. Bidet load still unknown. Working proposal
- **Entry controls (2-gang: ceiling + vanity light)** must not go in the pocket-door wall cavity. Put them on the solid jamb side. Electrical — decided
- **In tile:** centre each plate on a tile or on a grout line (3-in course) so cuts look intended. New suggestion

7 Laundry closet

Behind the Murphy bookcase door, next to the bathroom. Magicplan closet: 36 5/16 × 82⅝. No laundry photo in Magicplan.

- **Walls:** plain, washable satin, Pale Oak to match the hall. No moulding inside the closet. New suggestion
- **Two 120 V receptacles** for the LG WKG101HVA gas WashTower (washer and dryer each have a cord). Rename them LAUN-W and LAUN-D: “W1/W2” is already used by the kitchen range-wall outlets. New suggestion
- **Laundry protection, decided:** keep the planned dual-function (AFCI + GFCI) breakers on LAUN-W (20 A) and LAUN-D (15 A). Laundry-area receptacles and the washer and dryer themselves require GFCI protection under the 2023 NEC that California’s 2025 code adopts (210.8). LG’s “may not work properly on a GFI outlet” note does not override that; if a breaker nuisance-trips, check the device and cord rather than remove the protection. Electrical — decided
- **Reach:** both plugs reachable without pulling the tower out, clear of the water valves, and the Murphy bookcase shelves must close without hitting plugs. Exact height from the LG installation manual. Field check

8 Whole-unit outlet schedule

32 receptacle locations in the unit plus one attic service receptacle (furnace). Heights are box centres AFF; x is measured from the named reference.

ID	ROOM	WALL	POSITION	AFF	PLATE	STATUS
E1	Kitchen	East	6 N of SE corner	44	white, tile ring	Issued for bid
E2	Kitchen	East	48 N of SE corner	44	white, tile ring	Issued for bid
REF	Kitchen	East	74 N, behind fridge	15	white, tile ring	Issued for bid
S1	Kitchen	South	34 W of SE corner	39½	white, tile ring	Issued for bid
S2	Kitchen	South	84 W of SE corner	41	white, tile ring	Issued for bid
DW + GD	Kitchen	South	72 W, in sink base (2-gang)	14	white, tile ring	Issued for bid
W1	Kitchen	West	9 N of jog	44	white, tile ring	Issued for bid
W2	Kitchen	West	57 N of jog	44	white, tile ring	Issued for bid
RG	Kitchen	West	33¼ N, range rear zone	4	white, tile ring	Issued for bid
L1	Living	L01	x 17½	18	white, vertical	Working proposal
L2	Living	L01	x 106½	18	white, vertical	Working proposal
L3 / L4	Living	L03	side lower-frame centres	18	white, vertical	Working proposal
L5	Living	L04	not placed	18	white, vertical	Field check
L6	Living	L02	past pocket end only	18	white, vertical	Electrical — decided
D1 / D2	Dining	D01	(W+4)/4 · (3W−4)/4	18	white, vertical	Working proposal
D3 / D4	Dining	D02	side lower-frame centres	18	white, vertical	Working proposal
D5	Dining	D04	(3W−4)/4	18	white, vertical	New suggestion
D6	Dining	D03	past pocket end only	18	white, vertical	Electrical — decided
B1	Bedroom	A	17 from niche boundary	11½	dark, horizontal	Issued packet
B2	Bedroom	A	107 from niche boundary	11½	dark, horizontal	Issued packet

ID	ROOM	WALL	POSITION	AFF	PLATE	STATUS
B3	Bedroom	B	60½ from bay	11½	dark, horizontal	Issued packet
B4 / B5	Bedroom	desk / bay	budgeted, not placed	11½	dark, horizontal	Field check
H1	Hall	solid wall	clear of door swings	18	white, vertical	Working proposal
V1	Bath	vanity	≤36 from basin edge	40–44	GFCI	Working proposal
T1	Bath	toilet	beside tank	low	GFCI	Working proposal
LAUN-W / LAUN-D	Laundry	closet	behind tower, reachable	per LG manual	white	Electrical — decided

9 Sources

- Living & Dining Wall Treatments R2 (30 Oct 2026)
- Unit 4 Bedroom — Complete English Packet (12 Oct 2026)
- Unit 4 Bedroom — Complete Spanish Packet (12 Oct 2026)
- Electrical Plan Package Rev A (26 Oct 2026)
- Whole-Unit Electrical Working Plan (27 Oct 2026)
- Magicplan — Unit 4 MASTER plan
- LG WKG101H* pre-delivery sheet
- D04 interior coordination, kitchen doorway-infill framing R1 (2 Nov), bathroom TP1-R3a, CURRENT-DECISIONS — shared continuity folder.
- Photos: Magicplan MASTER plan room photos, 14 Oct 2026 (IMG numbers matched by file size to the R2 photo set).

Status key — Owner-confirmed: Tisa's direction. Issued packet / Issued for bid: a released document; use as written. Working proposal: earlier plan, not locked. New suggestion: first raised in this plan; Tisa locks or rejects. Field check: needs a site measurement before marking. Electrical — decided: our crew's electrical decision, based on code; rough-in still goes to city inspection.

English edition. A separate, synchronized Spanish edition exists; English governs on conflict.
