
Bathroom blocking - decide the marks before cutting

ONE DATUM: 0 AFF = TOP OF FINISHED FLOOR.

Floor build-up is UNKNOWN. Structural subfloor is below 0 AFF by an UNKNOWN amount. No approved mounting heights are recorded.

NTS: do not measure these pictures. Dashed items have no fixed size/position. Basis: John used the 21-page English R2 packet; page references below are to R2.

A BACK WALL - look toward tub

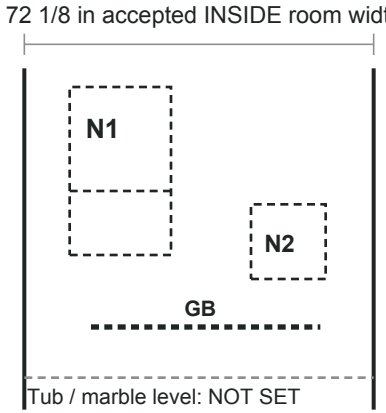

N1 LARGE NICHE

About 12 in wide × 20-24 in high; divider shelf.

Bottom AFF, shelf AFF, depth and position: NOT SET.

N2 SMALL NICHE

About 8-10 in square; toward controls.

Bottom AFF, depth and position: NOT SET.

0 AFF

Subfloor: offset UNKNOWN


N1 + N2 (pp10-11) TISA + JOHN: agree final finished sizes, bottom/shelf heights and horizontal positions. JOHN: check studs/services; allow for board, waterproofing and tile before rough openings are cut.

GB ONE HORIZONTAL BAR · pp11/16

Centerline AFF, length and mounting holes: NOT SET.

GB TISA: choose bar and height. INSTALLER: use its actual mounting pattern and required blocking/fasteners. Do not copy a height from the mockup.

B CONTROLS END - face right wall

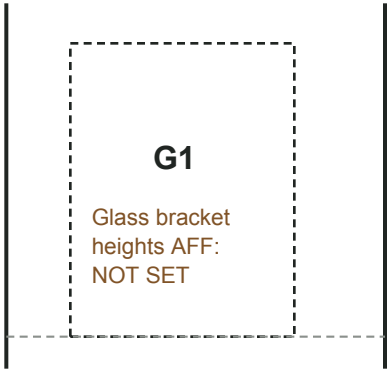

0 AFF


Subfloor: offset UNKNOWN

G1 CLEAR GLASS · pp16/19

G1 Controls end. GLASS INSTALLER: identify system, wall brackets and mounting locations; provide backing/anchor requirements. JOHN: leave those locations available until confirmed.

Do not use the mockup to set glass width, height or screw locations. Protect space for valve, spout and services; their offsets are not issued here.

C TUB / MARBLE - small section

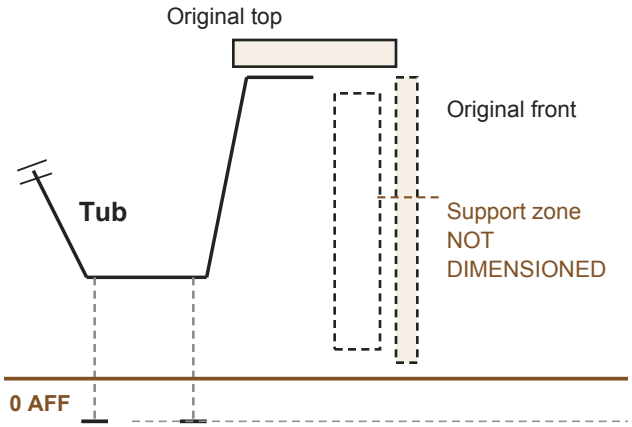

0 AFF

Subfloor: offset UNKNOWN

T1 TUB / STONE · pp1-6 / 12-15

DO NOW - JOHN: dry-fit tub/stone. Measure flange top/underside FROM SUBFLOOR; stone thicknesses, front height, overlap/joint, clear stud span. AFF awaits floor build-up; room width is not a frame cut.

Tub bears on feet/base; stone needs separate support/retention. R2 underside-minus-1/8 rule is UNRESOLVED, not a cut instruction. Producer/stone installer must resolve the support detail.

L1 WINDOW LEDGE · p11

TISA: confirm ledge height above marble. JOHN: measure actual finished width/depth. Height and cuts remain OPEN.

BEFORE FIXING THE FRONT OR CLOSING WALLS

SUPPORT CONFLICT: R2 pp2/4/6 set wood from the flange underside; pp12/14-15 require separate stone support. Resolve bearing/retention and front-frame setback from the fitted pieces before support cuts.

MISSING MARKS: hold final blocking locations pending the listed decisions. Measuring and product-pattern checks can proceed now. Keep drain access; resolve waterproof tie-in (p16) and photograph backing before closure.

English governs. Working coordination only; no final cuts, mount locations or structural support schedule released. All dimensions shown are inches.
