Unit 4 Bathroom — Installation Plan for John

1231 11th Avenue · English · Tub framing R2 (wood under the flange) · 14 October 2026 · Producer: Claude (Bathroom Producer)

John — the tub and marble, step by step

Who does what: JOHN · PLUMBER · ELECTRICIAN · TISA · PRODUCER. Lines with no tag are yours. The idea in one sentence: the tub sits on its own four feet; the wood goes under the tub flange and carries the marble top and the marble front; nothing hangs on the tub.

Step 1 — Measure, write down, send (before any cutting)

☐ JOHN Stand the tub on its feet on a flat floor. Measure floor to the top of the flange at both ends (catalog says 22 in — write what you measure), and floor to the underside of the flange (that is where the wood goes).

☐ JOHN Marble top: thickness, length, width. Set it dry on the tub and note how far it sticks out past the flange at the front and at each end.

☐ JOHN Marble front: height, thickness, length. Look at its top edge and the marble top's front edge: 45° miter, or square?

☐ JOHN Room: clear width between the bare studs on the tub wall.

☐ JOHN The rough edges: scrape one spot. Old glue comes off and leaves a clean edge; broken stone stays rough. Photo both.

☐ JOHN The extra strip of marble leaning at the left in your photo — what is it? Measure it, send a photo.

> **Send Tisa these numbers and photos. That is all we need from you before you build. Nothing else to survey.**

Step 2 — Set the tub

☐ JOHN Tub goes across the back wall, drain end against the controls wall (right). Push it to the controls-wall studs; whatever is left over goes to the window end and becomes the tile ledge.

☐ JOHN Tub on its four feet on the subfloor, shimmed level. Plastic film on the wood, then 1–2 in of mortar under the basin (Kohler). Put weight in the basin until the mortar sets. Never let the flange carry the tub.

☐ PLUMBER (or JOHN) Fit the K-7271 or K-7272 overflow/drain (Tub support & installation). Fill to the overflow, check every joint, drain, check again. Fix and repeat before anything is closed.

Step 3 — Wood under the flange (this carries the marble)

All of this wood goes UNDER the flange. Set the top of every piece at the underside of the flange less 1/8 in (measure it with the tub standing on its feet). After the tub is set and tested, pack that 1/8 in with hardwood shims so the flange is solidly backed everywhere the wood runs. The marble top then sits on the flange, and the flange sits on wood. Use 2×4 Douglas fir laid flat. See the drawings.

☐ JOHN Back wall: a 2×4 flat on the studs, full width of the room, under the back flange. Two #10 × 3 in structural screws into every stud.

☐ JOHN Controls-end wall: same thing, from the back wall to the front frame.

☐ JOHN Front: a short wall of 2×4s laid flat — a bottom plate on the subfloor, uprights every 12 in, a top plate — all on the flat so the whole thing is 1 1/2 in thick, standing under the front flange. Put 1/2 in exterior plywood on the room side. The plywood face sits 1/8 in inside the outer edge of the flange, so the marble front can stand in front of it, under the edge of the marble top. The frame is under the flange and does not touch the tub body.

☐ JOHN Window end: a 2×4 flat under the end flange, from the back wall to the front frame, on two short 2×4 legs. From there to the window wall, box in the leftover width for the tile ledge: a 2×4 on the window wall and a 3/4 in plywood top, set so the finished tile ends up a hair above the marble and drains onto it.

☐ JOHN Blocks under each corner of the marble top and behind the plywood where the marble front ends.

☐ JOHN Frame and block the two niches in the back wall now (big one about 12 wide × 20–24 tall with a shelf; small one about 8–10 square, over toward the controls — see Niches). Blocking for the grab bar and for the glass panel.

☐ TISA Decide how we get at the drain later (see Getting at the drain) before the controls-end wall is closed.

Step 4 — Marble top

☐ JOHN Clean the flange. 1/8 in bead of 100% silicone on the flange, at least 2 in in from the inside edge. Lower the top onto the wood; press down; weights overnight. Silicone the inside joint and tool it smooth. No construction adhesive or adhesive sealant between stone and tub — it has to stay separable.

Step 5 — Walls, waterproofing, wall tile

☐ JOHN Board and membrane on the three shower walls, the niches and the window ledge, everything sloped toward the tub. Photos before you cover anything.

☐ PRODUCER The detail where the wall membrane meets the marble top and the tub is not approved yet. You get it before that joint is closed. Waterproofing system: Waterproofing and backing.

☐ PLUMBER (or JOHN) Delta 144892-CZ-HS: the valve's plastic guard sits flush with the finished tile (±3/8 in). Tub spout drop is straight 1/2 in copper or iron, 8–18 in long, one 90° elbow, no PEX. Spout has to clear the marble and pour into the tub. Full detail: Delta shower and tub spout.

☐ ELECTRICIAN Receptacle, mirror lights, ceiling light, Panasonic FV-0511VQC1 fan (GFCI, 10 1/2 × 10 1/2 in ceiling cut, 6 in duct if possible). Nothing in the pocket-door wall or behind the medicine cabinet. Fan detail: Panasonic exhaust.

Step 6 — Floor tile, then the marble front


☐ TISA Pick the floor tile and the build-up (tile + mortar + underlayment). This is the one number that is not John's.

☐ JOHN Floor tile first. Then the marble front: dry-fit it. Its top edge meets the front edge of the marble top; its bottom should land on the finished floor with 1/8 in to spare. If it is too long, trim the bottom edge (nobody sees it). Then: silicone dabs on the plywood every 6 in, stand the front on 1/8 in shims on the tile, color-matched stone glue in the top joint, and silicone the floor joint after everything cures. The front stands on the floor; the glue at the top is a seal, not a hanger.

After that

Toilet, pedestal sink and faucet, medicine cabinet and lights (TISA chooses all of these), glass panel after the tile is done, crown and baseboards, final tests. Order of work: Construction sequence. Materials: Materials status.

Drawings and the few things to check

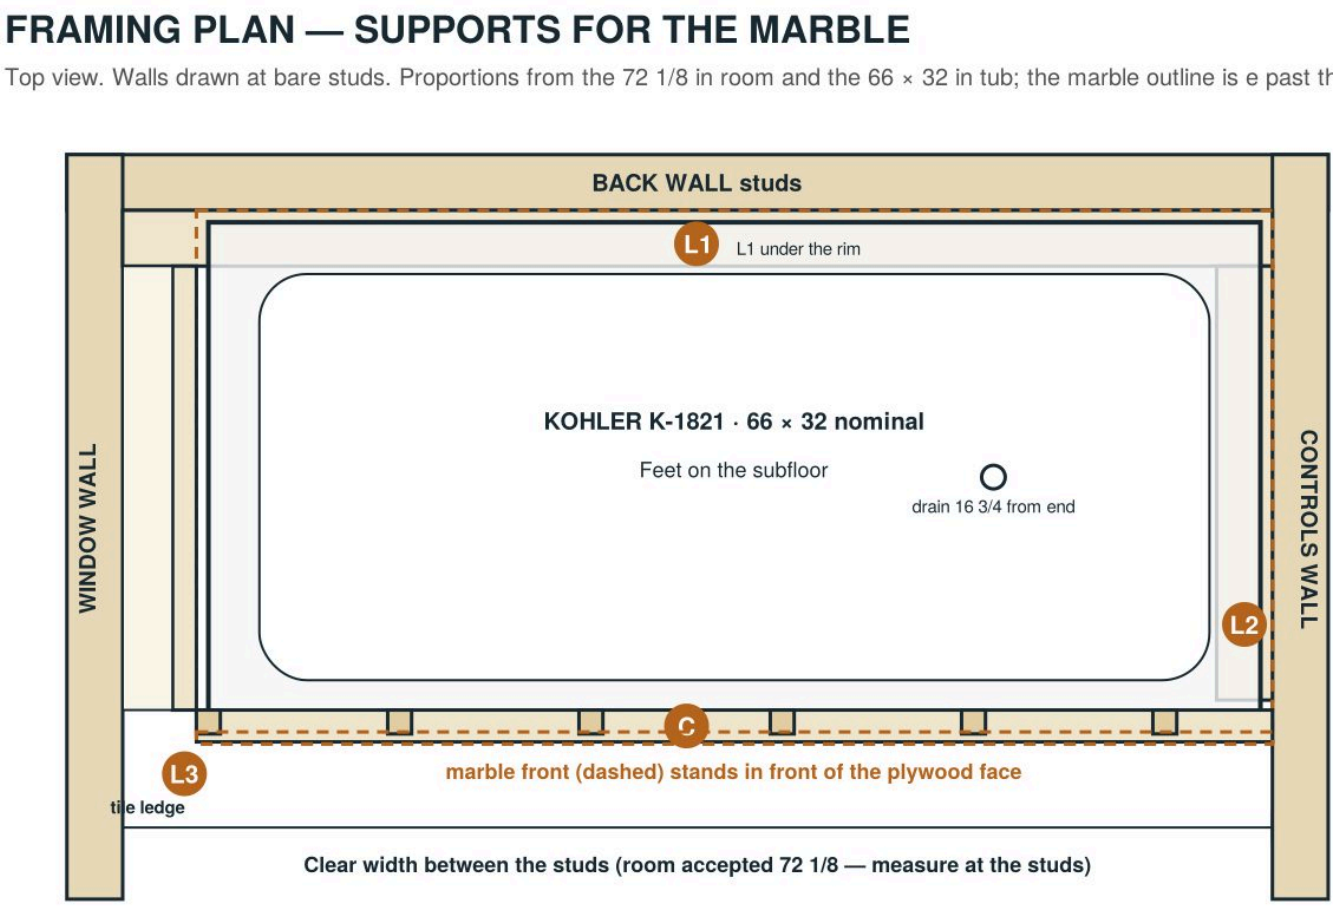


Framing plan

- **L1** Back wall: 2×4 flat on the studs under the back flange, full width of the room, top = underside of flange – 1/8. Two #10 × 3 in structural screws into every stud.
- **L2** Controls-end wall: 2×4 flat on those studs under the end flange, from L1 to the front frame, same height.
- **C** Front: short wall of 2×4s laid flat (plates + uprights every 12 in), standing under the front flange, same height, 1/2 in exterior plywood on the room side. Plywood face 1/8 in inside the outer edge of the flange; the marble front stands in front of it.
- **L3** Window end: 2×4 flat under the end flange, from L1 to the front frame, on two short 2×4 legs. Same height.
- **W** Tile ledge box: fills the leftover width to the window wall. 2×4 on the window wall + 3/4 in plywood top, then board + tile sloped toward the tub, finished tile a hair above the marble.
- **T** Tub pushed to the controls wall; all leftover width goes to the window ledge.

SECTION AT THE FRONT OF THE TUB (DRAIN END)

Looking along the tub. Not to scale. The wood goes under the flange; the marble top sits on the flange.

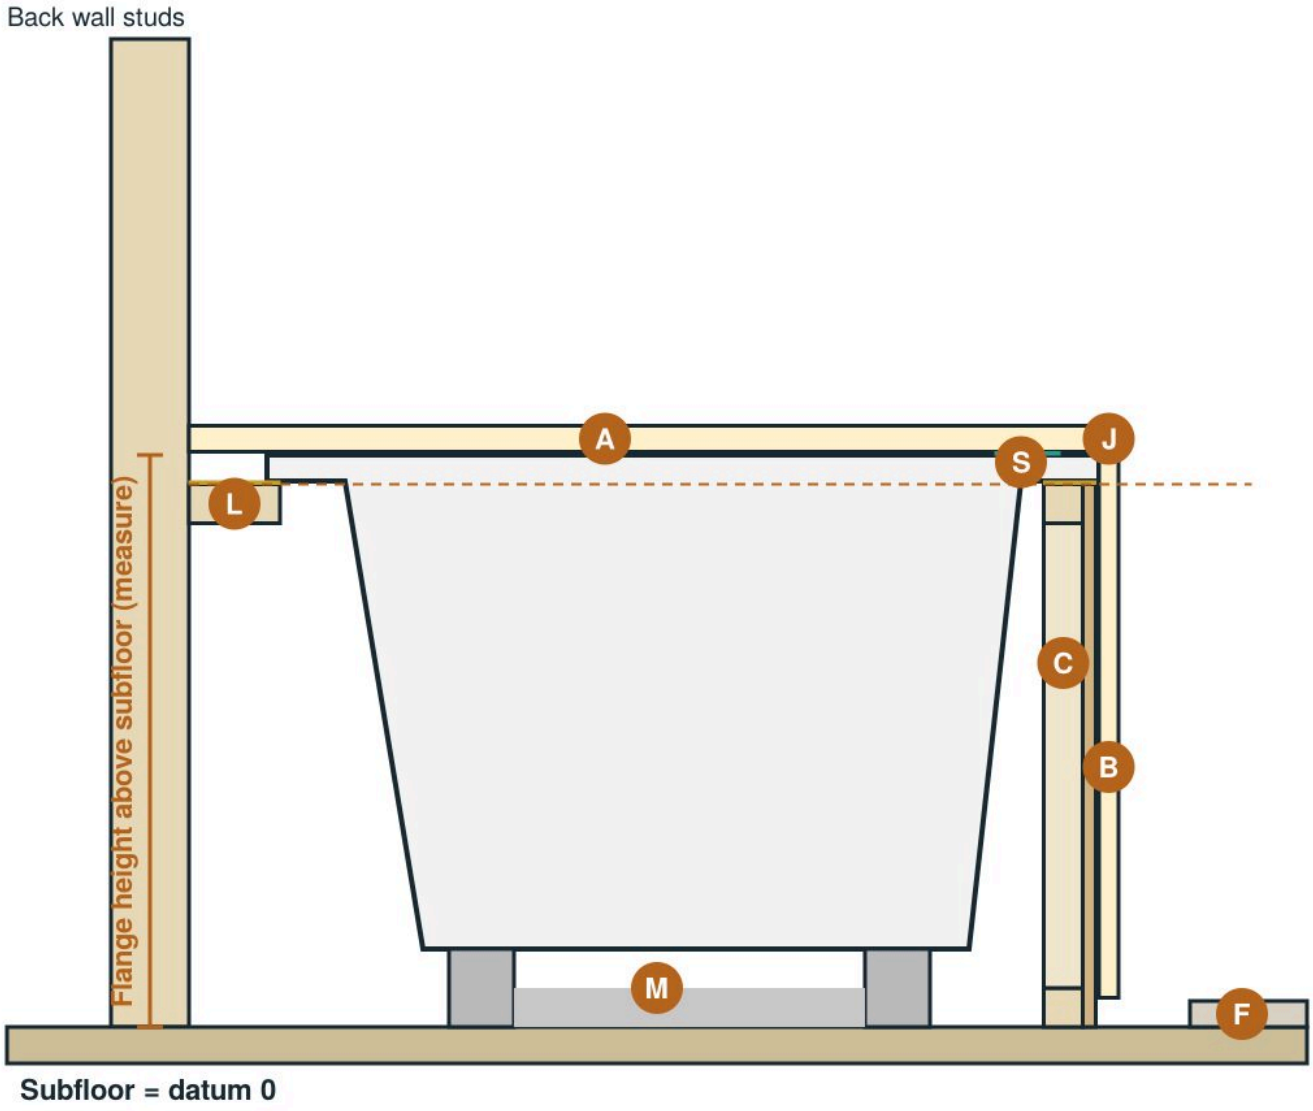

Loads: tub → its 4 feet → subfloor. marble top → flange → wood under the flange. marble front → fi

If the top sticks out past the flange less than the front is thick, the front would hit the flange: stop and tell the

Section at the front of the tub

- **A** Marble top. Sits on the tub flange on a bead of silicone.
- **S** 1/8 in bead of 100% silicone on the flange, at least 2 in from the inside edge (Kohler K-550). It seals only; it stays separable.
- **J** Top joint of the front: 45° miter or square — check the pieces. The top usually sticks out past the flange about as much as the front is thick.
- **B** Marble front. Stands on the finished floor on 1/8 in of silicone; silicone dabs hold it to the plywood.

- C Front frame under the flange: 2×4 on flat, uprights 12 in o.c., 1/2 in exterior plywood on the room face. Top of wood = underside of flange − 1/8, shimmed solid after the tub is set.
- L Back wall piece under the flange: 2×4 flat on the studs, top = underside of flange − 1/8, two #10 × 3 in screws per stud.
- M Tub on its 4 factory feet on the subfloor, shimmed level; 1–2 in mortar under the basin (Kohler). Never on the rim.
- F Finished floor (tile + mortar + underlayment): Tisa selects. The front goes on after the floor tile.

If the front comes out short or long

☐ Top of the marble top = flange height + 1/8 in silicone + marble-top thickness. Bottom of the front = that, minus the front's height (minus the top's thickness again if the joint is square, not mitered). It should land about 1/8 in above the finished floor.

☐ Front too long → trim its bottom edge. Front too short by more than 1/8 in → shim all four tub feet up by that amount BEFORE you mortar the tub. Never raise the tub to fix a long front.

☐ If the marble top sticks out past the flange LESS than the front is thick, the front will hit the flange. Stop and tell the producer before cutting anything.

Getting at the drain

Kohler wants access to the drain and the connections. The marble front is one solid piece, so access has to come through the controls-end wall (an opening from whatever room is behind it) or from below. TISA decides which. If neither works, every drain joint gets solvent-welded (no slip joints) and the front is set in silicone only, so it can be cut loose later. Do not close the controls-end wall until this is decided.

The rough edges

☐ Old glue: plastic scraper and a stone-safe remover. Do not grind the length of the edge. Chips: color-matched stone epoxy (AKEPOX 5010 is the candidate — PRODUCER buys it after a test on a hidden spot). The goal is a clean, discreet seam, not an invisible one.

☐ Stone to tub: 100% silicone only. Stone to stone (top to front): color-matched stone glue, on a front that is already standing on the floor.

Materials for the wood work

☐ 2×4 Douglas fir: back-wall piece as long as the room is wide; end piece and window-end piece about the width of the tub minus 5 in; two front plates as long as the tub; uprights, one per 12 in plus one, each (underside-of-flange height − 1/8 − 3) long; two short legs; blocking. One sheet 1/2 in exterior plywood for the front. Scrap 3/4 in plywood for the ledge top. #10 × 3 in structural screws (1 lb), 1 5/8 in screws, shims, one 60 lb bag of mortar, plastic film, 2 tubes 100% silicone. Stone glue: producer.



John’s photo, Oct 14: the marble top and front



John’s photo, Oct 14: the tub

Bathroom specifications and installation

Install the owned Kohler tub with its original marble top and front. This reference covers the assembly, plumbing, waterproofing, fixtures and finishes.




Design reference supplied by Tisa. Use for the intended look and arrangement; product examples and dimensions printed in the image still need verification.

From the entrance: pedestal sink left, toilet right and tub across the far wall. Marble covers the rim and front; warm ivory tile and Champagne Bronze complete the design. Keep one horizontal grab bar. Cabinet and lighting remain to select.

Bathroom layout

BATHROOM · LAYOUT REFERENCE

Accepted room dimensions · Indicative fixture arrangement

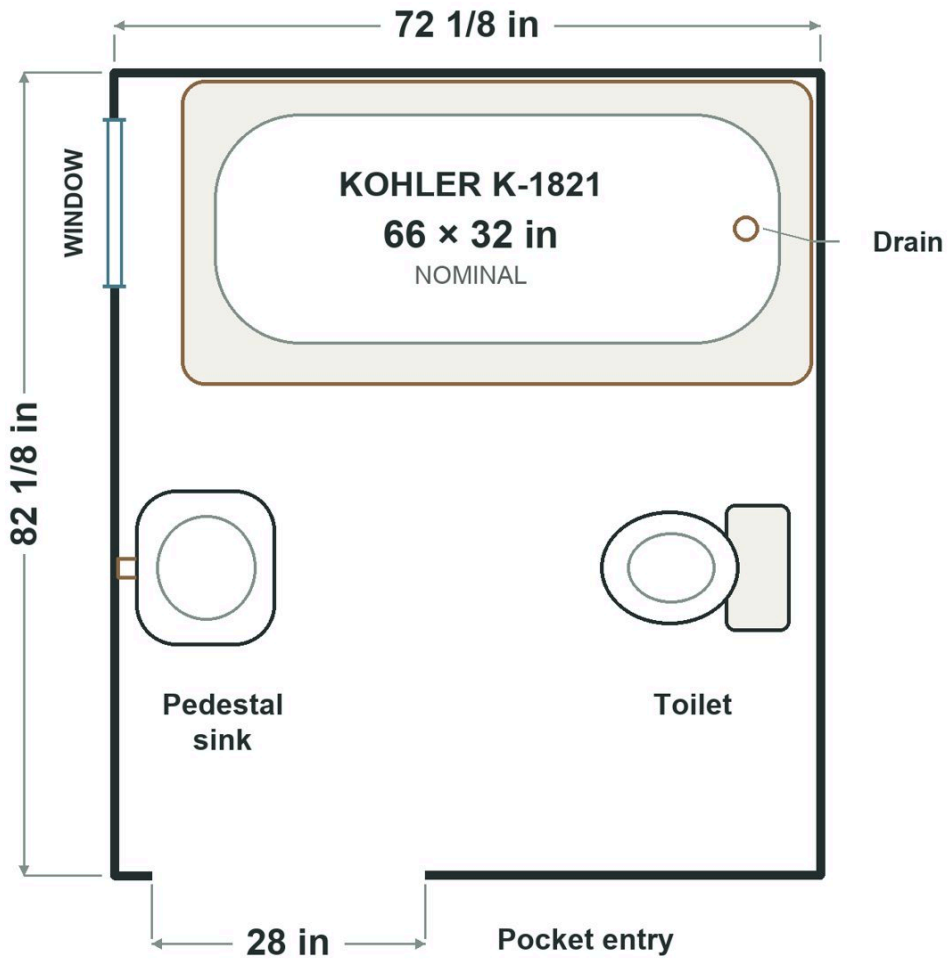

VERIFY BEFORE FABRICATION

Fixture offsets, window position and marble footprint are indicative. 72 1/8 − 66 = 6 1/8 in at the window end: arithmetic remainder only; this is NOT the finished ledge width. Confirm marble top/front fit, support and clearances on site. Not a construction drawing.


Source: Tisa-accepted Magicplan dimensions · Fixture arrangement schematic

Tisa's accepted room and doorway dimensions, with her fixture arrangement. Locations are indicative; the drawing does not set stone cuts or rough-in centers.

Use the locked 72⅛ × 82⅛-inch room and 28-inch entry. The screenshot's opposite edges differ by $\frac{1}{16}$ inch; keep the accepted locked values. Earlier $77\frac{3}{16}$ × 83⅛ and 81 × 74 model readings are superseded.

The bathtub implementation is unchanged. Retain the owned tub and both marble pieces. The pocket-door intent also remains; the source's swing symbol does not replace it.

Mirror & lighting options

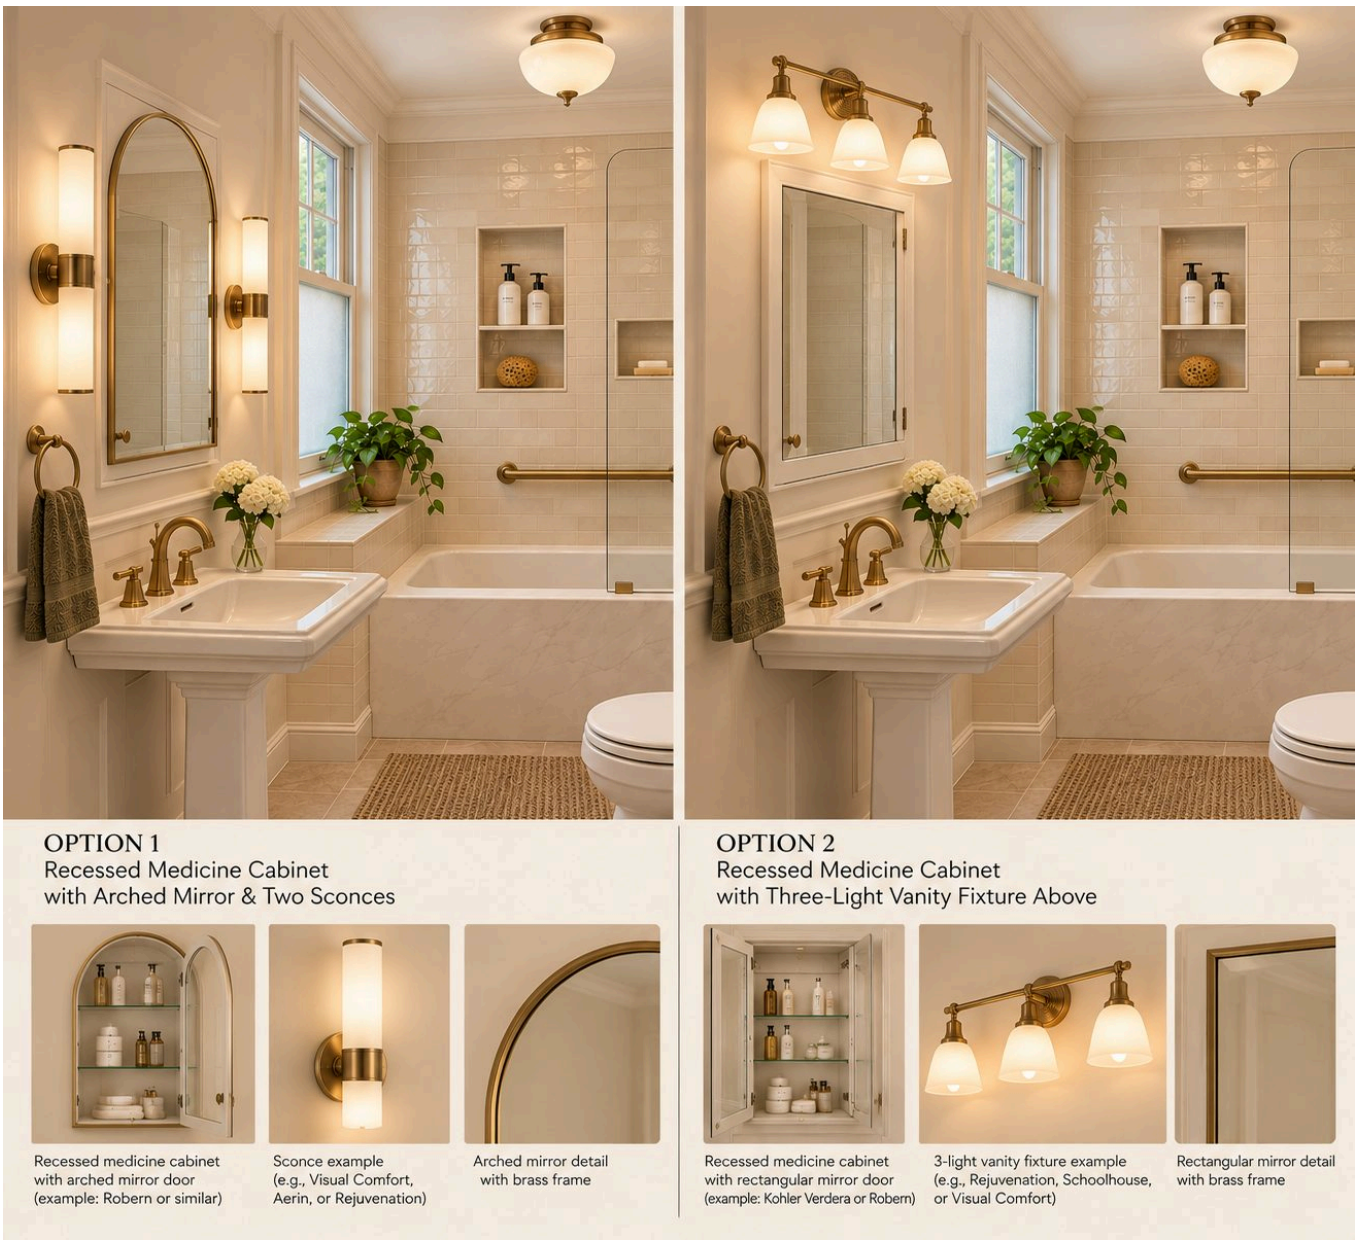

Two design alternatives, both supplied by Tisa. Neither lighting arrangement is recorded as the final selection.

Option 1: arched recessed cabinet with two side sconces. Option 2: rectangular recessed cabinet with a three-light fixture above.

The overview also shows Pottery Barn Vintage Inset and Kohler Verdera examples. Confirm the actual product, wall recess and sink centerline before choosing. The integrated-light option is a separate alternative.

Niches and finish details

Two recessed niches belong in the back shower wall; frame and block both before wall closure. Sizes below are approximate design targets. Coordinate finished openings, framing and elevations with the tile

layout; confirm clear-opening versus framed-size basis before cutting.

Large shampoo niche

QUANTITY 1 · 12 in wide × 20–24 in tall · Divider shelf

Provide space for shampoo, conditioner, body wash and bottles. Fit the divider to usable bottle heights and coordinate its elevation, niche depth and framing with the tile layout.

Small soap niche

QUANTITY 1 · Approximately 8–10 in square · Stagger toward controls

Use for bar soap and smaller toiletries, staggered toward the controls. Recess both niches into the back wall, waterproof them and slope horizontal surfaces toward the tub.

Window ledge and finishes

Window-end ledge: separate matching warm ivory tile, waterproofed and sloped toward the tub. Do not extend the waterfall marble over this ledge. Field-measure its finished width/depth and junctions; the 6⅛-in arithmetic remainder is not a cut dimension.

Shower walls: warm ivory ceramic. Floor: matte porcelain with a warm limestone appearance. Select tile size, grout, profiles and layout; prepare quantities from measured coverage.

Moldings and accessories

Traditional crown surrounds the ceiling, including above the window where clearance permits. Fit its profile within that clearance; baseboards run along dry walls. Provide one horizontal grab bar with backing, towel accessories and a toilet-paper holder; lengths and locations follow selected products.

Wainscoting remains under consideration. Prepare its layout and price; do not purchase or install without Tisa’s approval. Record niche dimensions and placement on the existing project board.

Pedestal sink and cabinet setup

OWNED · One pedestal sink · Champagne Bronze faucet to select

Install the retained pedestal on the left wall. Center the medicine cabinet and lighting on the sink; use the actual basin, pedestal and fixing pattern to establish the installation.

Sink and faucet

- The retained basin and pedestal determine overall width, projection and installed height; their original mounting points control fixing locations.
- Set the sink against the finished wall, allowing for the P-trap, supplies and accessible shutoffs. Keep its centerline coordinated with the mirror and lights.
- Match the Champagne Bronze faucet to the basin’s existing hole count and spacing, with suitable reach into the bowl. Use the basin’s drain opening and mounting pattern.

Cabinet wall and recess

- Size the cabinet within the wall width above the sink and the space between basin and ceiling; allow for door swing and either side sconces or an overhead light.

- The recess must fit between structural framing and clear pipes, wiring and ventilation. Establish usable cavity depth before cabinet purchase; do not cut structural members to suit a rendering.

Confirm the cabinet and lights

A recessed arched mirror medicine cabinet remains an option. Cabinet overall size, rough opening, depth and hinge clearance come from the selected model. The supplied images are selection references.

Lighting choices: two sconces flanking the mirror, or one three-light fixture above. Rectangular and integrated-light alternatives also appear in the boards. Coordinate boxes with the chosen fixture dimensions and cabinet centerline.

Select a compatible Champagne Bronze faucet for the owned pedestal. Confirm faucet reach, hole configuration, drain, P-trap, supply lines, shutoffs and mounting hardware before buying.

Selection detail: no current pedestal model or cabinet model is established in the records. Their actual fixing/connection patterns and selected cabinet rough opening govern installation; old rendering offsets are not rough-in coordinates.

Assembly interfaces and checks

Scope: retain the tub, original marble top and exposed front; build a separately supported stone surround with continuous wet-area waterproofing, coordinated plumbing and service access.

Trade interfaces

- The tub bears through its factory feet/base to the supported floor. The marble top and front have their own bearing and retention. Fit the original pieces together to establish the surround geometry; the finished stone height includes the existing top and its joint above the tub rim.
- Plumbing connects the K-7271/K-7272 slotted-overflow drain and the purchased Delta valve/spout to the finished assembly. Electrical rough-in includes the fan, mirror lights and receptacle. Waterproofing continues through niches, window return and the stone/tub junction. Glass is templated after finishes.

Construction checks

- Use the original top and front as fitting templates for stone supports. Preserve separate tub and stone load paths, the rim-covering design and a usable drain-access route. Set support elevation from the assembled pieces, not from 22 inches alone.
- Before closing walls/front: plumbing and electrical rough-in accepted, backing photographed, water connections tested, and the wall–stone–tub waterproof junction resolved and inspected.
- Before glass: stone/tile fixed and cured; final dimensions and anchor substrates measured. Before handover: complete the functional checks and repair any leaks or defects.

Concealed work record

Keep installation photos of the concealed supports, drain/overflow and Delta connections, fixture blocking and continuous waterproofing before closure. They support later service and inspection; no separate measurement submission is required to proceed.

Materials to stage

Keep the owned tub, top and front together. Check drain/overflow parts, supplied Delta valve/spout, bedding product, stone supports/retention, removable silicone joint, selected membrane kit, tile/mortar/grout and flexible joints. Quantities for framing, tile and stone repairs follow the recorded assembly and measured takeoff; use the purchase list after checking stock.

The project producer manages scheduling, material decisions, missing information and the existing task board. Conflicts discovered during fitting belong at the affected detail; the installation sequence below remains the working plan.

Owned tub & original marble



John's October 14 photos: the owned tub, and its separate original top surround and front panel. Both marble pieces belong in the installation assembly.

Kohler Underscore K-1821: acrylic, nominal 66 × 32 × 22 in. Drain center: 16¾ in from the drain-end outer edge and 16 in across the 32-in width. Outlet: 1½ in. Required slotted-overflow drain: K-7271 or K-7272.

Original assembly

- The original surround and front are owned. Remove old adhesive and dry-fit their original edge relationship. Repair chips and minimally true jagged mating edges while preserving dimensions; do not automatically grind full lengths or recut new 45° miters.
- Place the tub across the far wall, drain at the controls end. Fit the original marble over the rim and at the exposed front. The separate window-end ledge is ivory tile, waterproofed and sloped toward the

tub.


- Finished height follows the tub's bearing elevation, nominal 22-in tub height, top thickness and actual stone/rim joint. Relate the front's lower edge to the finished floor; retain drain access behind or below the front.

Local detail: numerical stone thickness, cut profile and front height are absent from the records; fit the retained pieces. Support/retention and the custom waterproof tie-in remain project details. A discreet restored seam is the aim, not a guaranteed invisible joint.

Tub support & installation

SECTION AT THE FRONT OF THE TUB (DRAIN END)

Looking along the tub. Not to scale. The wood goes under the flange; the marble top sits on the flange.

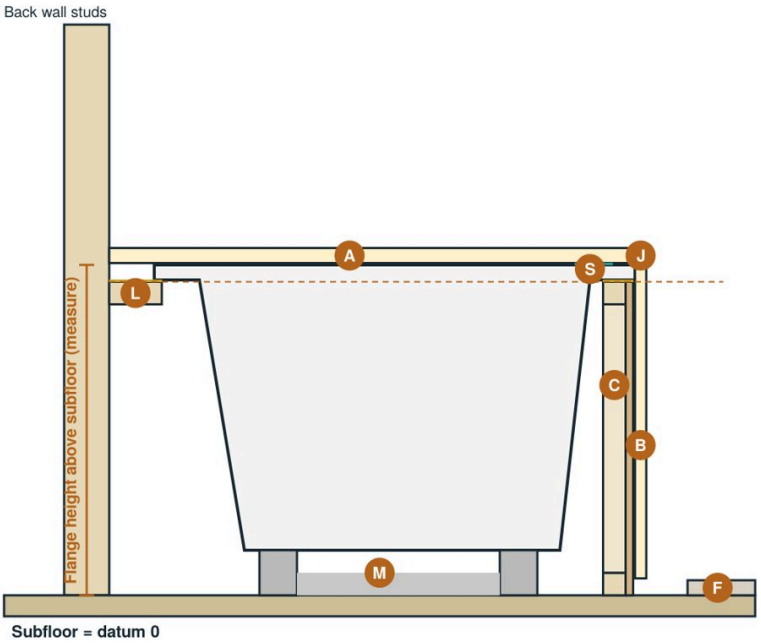

- **A / S** Marble top. Sits on the tub flange on a bead of silicone. 1/8 in bead of 100% silicone on the flange, at least 2 in from the inside edge (Kohler K-550). It seals only; it stays separable.
- **J** Top joint of the front: 45° miter or square — check the pieces. The top usually sticks out past the flange about as much as the front is thick.
- **B** Marble front. Stands on the finished floor on 1/8 in of silicone; silicone dabs hold it to the plywood.
- **C** Front frame under the flange: 2×4 on flat, uprights 12 in o.c., 1/2 in exterior plywood on the room face. Top of wood = underside of flange − 1/8, shimmed solid after the tub is set.
- **L** Back wall piece under the flange: 2×4 flat on the studs, top = underside of flange − 1/8, two #10 × 3 in screws per stud.
- **M** Tub on its 4 factory feet on the subfloor, shimmed level; 1–2 in mortar under the basin (Kohler). Never on the rim.
- **F** Finished floor (tile + mortar + underlayment): Tisa selects. The front goes on after the floor tile.

Loads: tub → its 4 feet → subfloor. marble top → flange → wood under the flange. marble front → finished floor + plywood.

If the top sticks out past the flange less than the front is thick, the front would hit the flange: stop and tell the producer before cutting anything.

Set out and support

- Use a level, adequately supported floor. Tub plus full water is about 802 lb, before bather, marble and framing; support the complete assembly.
- Provide separate bracing for the original top and support/retention for its front. Keep drain access. K-550 is the undermount template/guide basis; the 64½ × 30½-in drop-in opening is not a stone-cutting template.
- Fit the K-7271/K-7272 drain and align the rough drain. Kohler permits a 1–2-in mortar-cement bed or compatible construction adhesive at the feet/base. The rim does not carry the tub.
- Level on the factory feet/base and follow bedding cure/loading instructions. The guide's ⅛-in spacers illustrate drop-in installation; they do not set this stone-over-rim support height.

Test, then fit the stone

- Connect with joints visible. Fill to the overflow, check the overflow and every connection, then drain and inspect again. Repair leaks and repeat before front closure.
- Fit the existing stone opening using the K-550 reveal/template detail. Use a removable silicone joint, not adhesive sealant bonding stone permanently to the tub. Its bedding bead stays at least 2 in from the inner well edge.
- Complete the wall–stone–tub waterproof junction and stone joint; secure the front on its own support/retention while keeping service access. Protect the tub through finishing.

Manufacturer basis: Kohler K-1821 specification; bath guide 1084212-2-H; undermount guide 114753-2-CD. John's older 1023730-2-F is retained as background, not the K-1821 setting detail.

Plumbing, electrical & ventilation

Delta shower and tub spout

- Use the purchased 144892-CZ-HS assembly. Confirm the supplied R10000 valve suffix and spout adapter. Make a sample of board, waterproofing, mortar and actual tile; set valve depth from that finished wall face. Set the plasterguard flush with finished tile, within ±⅜ inch; with integral stops, flush to ⅜ inch behind.
- Valve UP arrow faces up; shower outlet is above, tub outlet below. The tub-spout drop must be straight ½-inch copper/iron, 8–18 inches long, with one 90° copper/iron elbow. No PEX in this drop; no deck-mounted substitute spout.
- Dry-fit the spout against the marble and finished wall plane before fixing heights. Confirm the discharge clears the stone and enters the basin. Check handle/hose operation and glass clearance. Use the supplied spout's actual stub-out instruction.
- Flush as the Delta guide directs, assemble and leak-test before closure. At commissioning, confirm cold first and set the rotational limit with a thermometer to no more than 120°F, or a lower applicable limit.

Sink, toilet and electrical layout

Use the compatible slotted-overflow drain, adapters and any necessary modification to existing plumbing. Match faucet holes, drain, P-trap, supplies, shutoffs and mounting to the retained pedestal. A new toilet is needed; model not selected. Existing rough-in and clearances govern selection and connection/adapter requirements. Keep shutoffs accessible.

Electrician: mark the circuit and final locations for receptacle, mirror lights, ceiling light and fan/control. Coordinate required GFCI protection, wet-area fixture ratings and inspection with the electrical package. Keep wiring and boxes out of the pocket cavity and medicine-cabinet recess.

Panasonic exhaust

FV-0511VQC1: 120 V, 60 Hz, grounded; no integral light. Use a dedicated exterior exhaust, preferably a short route with 6-inch-diameter duct; 4-inch-diameter duct is also manufacturer-permitted. Secure/seal joints, insulate attic duct, remove damper shipping tape and provide exterior backdraft protection. No solid-state speed controller or dimmer; sensors need power during normal operation.

Confirm joists and the 10½ × 10½-inch square ceiling opening before cutting. Above-tub mounting requires GFCI-protected supply. Start at 80 CFM / 20-minute delay / about 50% RH, then measure airflow and tune. Verify sensing and replacement air with the pocket door closed.

Installation references: Delta 107528 Rev I; Panasonic FV-0511VQC1 English and Spanish.

Waterproofing and backing

One coordinated wet-area assembly

Proposed system: Schluter KERDI-BOARD, KERDI-BAND, compatible corners/penetration seals, KERDI-FIX and ALL-SET. Check stock first. This is a coherent proposal; record the selected complete system before ordering or mixing materials.

- Prepare sound framing. Proposed board: ½ inch at studs up to 16 inches on center, ¾ inch at 24 inches. Use system screws/washers, maximum 12-inch wall spacing and screw penetration of at least ¾ inch into wood or ⅜ inch into metal studs. Add backing for niches, grab bar, glass and fixtures before covering.
- Seal seams, corners, fasteners and penetrations; maintain 2-inch membrane overlaps and carry waterproofing at least to showerhead height. Form both niches and the separate window ledge with surfaces draining toward the tub.
- Local detail pending — project producer: wall membrane → marble deck → tub termination. This stone-over-rim assembly is not Schluter's standard flanged-tub detail. The exact compatible tie-in is not yet specified; complete that detail before closing this interface. Exposed caulk is only the finish joint.

Tile stone and clear glass

- Record wall tile, floor tile, size, grout joint/color, edge profiles and mortar compatibility. Make a layout showing window, two staggered niches and the exposed stone edge. Use balanced cuts; agree visible joints before setting. Lift sample tiles to verify at least 95% mortar coverage in wet areas. Use compatible flexible joints/profiles at inside corners and material transitions rather than hard grout.
- Confirm the floor's actual subfloor, stiffness, underlayment and finished height before tiling. Select its complete supported assembly; the wall-board specification is not a floor build-up. Measure net exposed coverage and carton yield.
- Inspect and photograph waterproofing before covering it. Install stone and adjacent tile in the sequence shown in the accepted wall–stone–tub section. Inspect the concealed waterproof connection before closure. Do not remove a sealed stone top for later tile work. Install the floor and respect curing times.

Glass and finish acceptance

After tile and marble are fixed and cured, the glass installer measures the partial clear-glass panel at the controls end and specifies safety glass, thickness, clamps/channel and anchors. Check the spout, hand shower, cleaning and entry. No improvised drilling through the stone, tub or horizontal waterproofing.

Install chosen medicine cabinet/lights, toilet, pedestal, accessories, crown and baseboards. Check window clearance, door travel, all water/drain connections, fan flow, lighting and shower temperature.

Save test records, concealed-work photos and finished views; close each punch item.

Waterproofing reference: Schluter Shower System Handbook, bathtub surrounds, niches and KERDI-BOARD sections. Product selections and the special stone/tub termination must match the actual assembly.

Materials status and next purchases

Check stock before buying. Unknown dimensions/quantities remain field tasks; inventory determines the final missing order.

Tub

OWNED · 1 unit

Kohler K-1821 model basis; nominal 66 × 32 × 22 in. Verify actual label, feet/base and drain centers. Reuse; protect during work.

Original marble top and front

OWNED · 1 top + 1 front

Reuse both original pieces as fitting templates. The existing opening, edge profile, thickness and condition govern support, fitting and any repair; no replacement stone is specified.

Pedestal sink and door slab

OWNED · 1 sink + 1 retained door slab

Measure sink and faucet holes. Reuse door slab: Ervin reports 27¼ × 79⅜ in. Thickness and hardware belong to the separate pocket-door packet; John is not assigned that work.

Delta Arcadia shower set

ORDERED · 1 set · Delivery unconfirmed

144892-CZ-HS, Champagne Bronze, valve included. Lowe's $291.54 including tax; shipped October 13, original ETA October 19. Inventory every included component and list only missing parts.

Panasonic exhaust fan

DELIVERED · 1 unit · Installation unverified

WhisperSense FV-0511VQC1. Home Depot $243.31 including tax; delivered September 15. Verify retained unit, duct/cap, control, power and operation.

New toilet — model not selected

NEED TO PURCHASE · 1 new toilet

Measure the existing rough-in and actual clearances for selection. Confirm model, connection/adapter and seat before purchase or flange work.

Materials for rough work

Check stock before buying. Unknown dimensions/quantities remain field tasks; inventory determines the final missing order.

Tub drain and overflow

NEED TO BUY AFTER INVENTORY · 1 compatible assembly

K-7271 or K-7272 slotted-overflow drain for K-1821. Reuse compatible retained parts; add only missing drain pieces and adapters required by the actual plumbing connection.

Pedestal faucet and drainage

NEED TO BUY AFTER INVENTORY · 1 faucet + 1 drain + 1 P-trap

Champagne Bronze faucet matched to measured holes and reach. Verify retained drainage parts and sizes before ordering.

Sink supplies shutoffs and fixing

NEED TO BUY AFTER INVENTORY · Quantities to confirm

List hot/cold supply connections, shutoffs, adapters and mounting hardware individually after checking the actual sink and existing rough-in.

Tub and stone support materials

NEED TO BUY AFTER INVENTORY · Measured takeoff pending

Bedding: mortar or permitted adhesive at factory feet/base; independent stone bracing and front retention. Stone-to-stone seam candidate, not purchased: AKEPOX 5010 Coloured. Clean/slightly roughen bonding faces; trial color/staining on a concealed area of the actual stone. Mix 2:1; at 20°C allow 20–30 min working time, 6–8 h before moving, 12–16 h before processing and 7 days to full stability. Restore the local finish after cure. Stone adhesive does not replace support or the separable marble-to-acrylic silicone joint.

Waterproofing and niche framing

PROPOSED · Stock and quantities unverified

KERDI-BOARD/BAND, corners/seals, KERDI-FIX and ALL-SET proposal. Record chosen complete system, panel thickness, membrane area/overlaps, fasteners, niche framing/blocking and sealant quantities.

Pocket door and ventilation materials

NEED TO BUY AFTER INVENTORY · Quantities to confirm

Pocket frame/privacy hardware and missing jamb/trim per separate door packet. Fan duct/cap: measure route and diameter; inventory fittings, sealing/insulation and controls.

Materials for finishes

Check stock before buying. Unknown dimensions/quantities remain field tasks; inventory determines the final missing order.

Shower walls and window ledge

NEED TO BUY AFTER INVENTORY

Warm ivory ceramic. Record product, size, layout, net area, cuts, waste allowance, carton yield and cartons. Include both niches and separate sloped window ledge.

Bathroom floor

NEED TO BUY AFTER INVENTORY

Warm limestone-look matte porcelain. Record exposed floor area, tile size, underlayment, finished height, threshold, waste allowance and cartons.

Tile setting and edge materials

NEED TO BUY AFTER INVENTORY

Compatible mortar, grout/color, flexible sealant, profiles and transitions. Record joint sizes, profile lengths and product coverage-based quantities.

Partial clear-glass screen

NEED TO BUY · 1 panel after finished measurement

Controls end; record final width/height, safety-glass thickness, hardware finish, anchors and clearances. Glass installer provides template and fixing detail.

Medicine cabinet and lighting

NEED TO BUY AFTER INVENTORY · Selection pending

One recessed cabinet, size after wall/sink survey. Choose two side sconces or one three-light fixture above; confirm ceiling light, controls, fixture sizes and quantities.

Crown baseboards and accessories

NEED TO BUY AFTER INVENTORY

Measure crown/baseboard profiles and lengths, including conditional crown above window. One horizontal grab bar; choose length/location. Record towel bars/ring, paper holder and fixing quantities.

Decorative wainscoting

ON HOLD · No purchase or installation

Tisa’s approval is required after a detailed layout and price. Do not include it as an approved finish order.

Construction sequence

Follow these ten construction stages. The project producer manages scheduling, material decisions and unresolved information in the existing task system.

- Confirm bathtub dimensions, framing, drain locations and rough plumbing. Include the owned top/front, measured support section and spout reach.
- Frame and block both shower niches before closing the walls. Coordinate their approximate 12 × 20–24-in and 8–10-in targets with finished openings and tile joints.
- Complete plumbing and electrical rough-ins, including preparation for the recessed medicine cabinet and lighting. Verify feasibility, included Delta components and concealed-work photos.
- Install, secure and test the bathtub using its feet/base support. Inspect visible drain/overflow connections through filling and discharge; repair and retest before closure.

- Complete waterproofing and prepare shower walls and floor. Inspect the selected system and resolve the wall–stone–tub junction before it is concealed.
- Coordinate and install shower tile, original waterfall marble top/front and the separate tiled window ledge. Follow the accepted junction section and maintain the ledge/niche slopes.
- Install bathroom floor tile over the verified floor assembly. Respect the chosen products' curing requirements.
- Install the toilet, pedestal sink, faucets, lighting and accessories after their relevant finishes are complete. Check mounting, connections and operation.
- Take final measurements and install the partial clear-glass screen at the controls end. Verify anchors, spout/hand-shower clearance, entry and cleaning access.
- Complete moldings, caulking and finishing work. Test water/drains, shower controls/temperature, exhaust, lighting and door; record final photos and close defects.

Site photos & field checks



Ervin's photos, sent October 14: bathroom entrance, exposed framing and the adjacent wall from two hall viewpoints. These show current conditions, not completed work or measured clearances.

Installation context

- Room: accepted dimensions are 72⅛ × 82⅛ inches, doorway 28 inches, from Tisa's trusted October 14 screenshot. John's interior annotations agree. Keep these governing dimensions; the forked Magicplan correction is separate from this unchanged tub installation scope.

- The tub assembly uses the K-1821 dimensions and original stone fitting described in this plan. Toilet selection depends on existing rough-in and clearances; glass fabrication follows completed tile and stone.
- The retained sink’s real footprint, fixing and faucet-hole pattern govern its installation. Cabinet and lighting fit the available wall/cavity above it, clear of framing, plumbing, electrical and ventilation.
- Pocket door: far-left opening; leaf slides right viewed from the hall. Reuse the slab. Measurements and hardware are coordinated in the separate door package; this work is not assigned to John.

Source records: Bathroom Production Package • Bathroom Tiling Detail. Purchases checked against Lowe’s order/shipment and Home Depot delivery records; design boards supplied by Tisa.

The project producer maintains design decisions, purchasing and construction priorities in the existing task system. Site photos document conditions and concealed installation; they are not substitute dimensions.
